


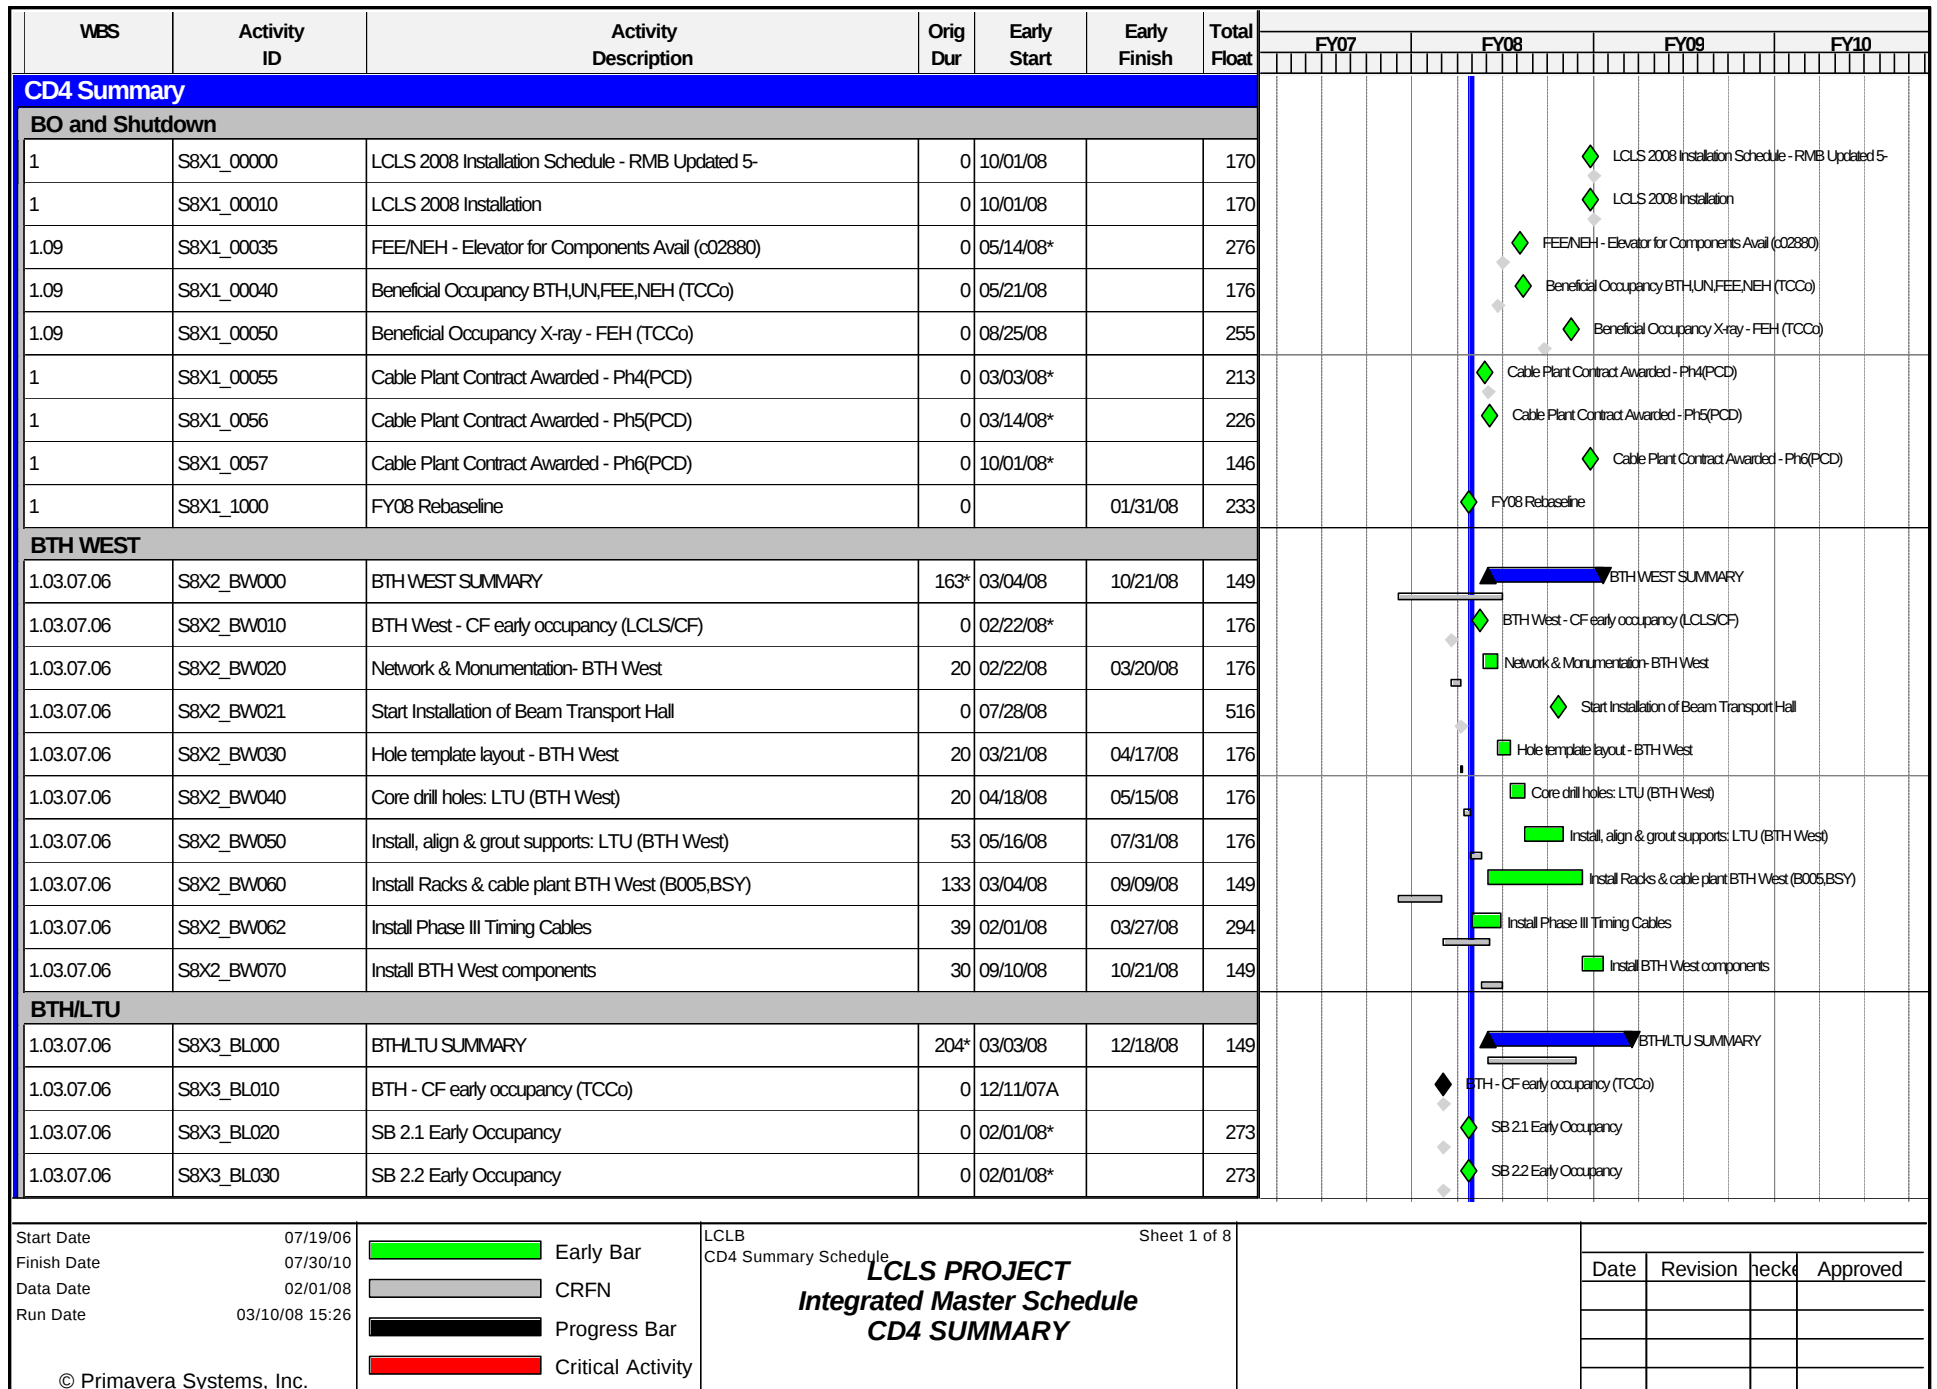

Start Date 07/19/06
 Finish Date 07/30/10
 Data Date 02/01/08
 Run Date 03/10/08 15:26

Early Bar
 CRFN
 Progress Bar
 Critical Activity

LCLB
 CD4 Summary Schedule
LCLS PROJECT
Integrated Master Schedule
CD4 SUMMARY

Sheet 1 of 8

Date	Revision	check	Approved

WBS	Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float	FY07				FY08				FY09				FY10			
NEAR EXPERIMENTAL HALL (NEH)																						
1.06.06.02.09	S8X7_NH611	ED&I for LBL Timing Fiber (PCD-Ph6)	128	04/01/08*	09/30/08	347	 ED&I for LBL Timing Fiber (PCD-Ph6)															
1.06.06.02.09	S8X7_NH612	Install LBL Timing Fiber NEH (PCD-Ph6)	40	10/29/08	12/26/08	287	 Install LBL Timing Fiber NEH (PCD-Ph6)															
1.06.06.02.06	S8Z1_PB059	ED&I for PPS Cabling - FEE/NEH (PCD-Ph6)	128	04/01/08*	09/30/08	204	 ED&I for PPS Cabling - FEE/NEH (PCD-Ph6)															
X-RAY TUNNEL																						
1	S8X8_XT000	X-RAY TUNNEL SUMMARY	319*	07/23/08	10/20/09	112	 X-RAY TUNNEL SUMMARY															
1.05.06.03	S8X8_XT010	X-Ray Tunnel - CF early occupancy (TCCo)	0	07/23/08*		180	 X-Ray Tunnel - CF early occupancy (TCCo)															
1.05.06.03	S8X8_XT020	Network & Monumentation- X-ray tunnel	10	10/02/08	10/15/08	130	 Network & Monumentation- X-ray tunnel															
1.05.06.03	S8X8_XT030	Hole template layout - X-ray tunnel	5	10/16/08	10/22/08	226	 Hole template layout - X-ray tunnel															
1.05.06.03	S8X8_XT040	Core drill holes: X-Ray tunnel	10	10/23/08	11/05/08	226	 Core drill holes: X-Ray tunnel															
1.05.06.03	S8X8_XT050	Install, align & grout supports: X-ray	20	11/06/08	12/05/08	226	 Install, align & grout supports: X-ray															
1.05.06.03	S8X8_XT060	Install Racks & cable plant X-Ray	60	12/08/08	03/03/09	226	 Install Racks & cable plant X-Ray															
1.05.06.03	S8X8_XT065	XT Start Tunnel Installation	0	03/26/09		220	 XT Start Tunnel Installation															
1.05.06.03	S8X8_XT070	Install X-ray tunnel components - XT	30	03/26/09	05/06/09	190	 Install X-ray tunnel components - XT															
1.06.06.03	S8X8_XT080	Install X-Ray tunnel components - XE	20	07/29/09	08/25/09	112	 Install X-Ray tunnel components - XE															
1.05.06.03	S8X8_XT090	Terminate cable plant X-Ray	20	08/26/09	09/22/09	112	 Terminate cable plant X-Ray															
1.05.06.03	S8X8_XT100	Checkout X-Ray tunnel systems - XT	10	09/23/09	10/06/09	122	 Checkout X-Ray tunnel systems - XT															
1.06.06.03	S8X8_XT110	Checkout X-Ray tunnel systems - XE	20	09/23/09	10/20/09	112	 Checkout X-Ray tunnel systems - XE															
FAR EXPERIMENTAL HALL (FEH)																						
1.05.06.02	S8X7_NH066	XT Start Installation in NEH	0	02/09/09		381	 XT Start Installation in NEH															
1	S8X9_FH000	FEH SUMMARY	329*	07/23/08	11/03/09	112	 FEH SUMMARY															
1.06.06.04	S8X9_FH010	FEH - CF early occupancy (TCCo)	0	07/23/08		190	 FEH - CF early occupancy (TCCo)															
1.05.06.04	S8X9_FH020	Network & Monumentation- FEH	5	10/16/08	10/22/08	130	 Network & Monumentation- FEH															
1.05.06.04	S8X9_FH030	Hole template layout - FEH	2	10/23/08	10/24/08	130	 Hole template layout - FEH															
1.05.06.04	S8X9_FH040	Core drill holes: FEH	5	10/27/08	10/31/08	130																

