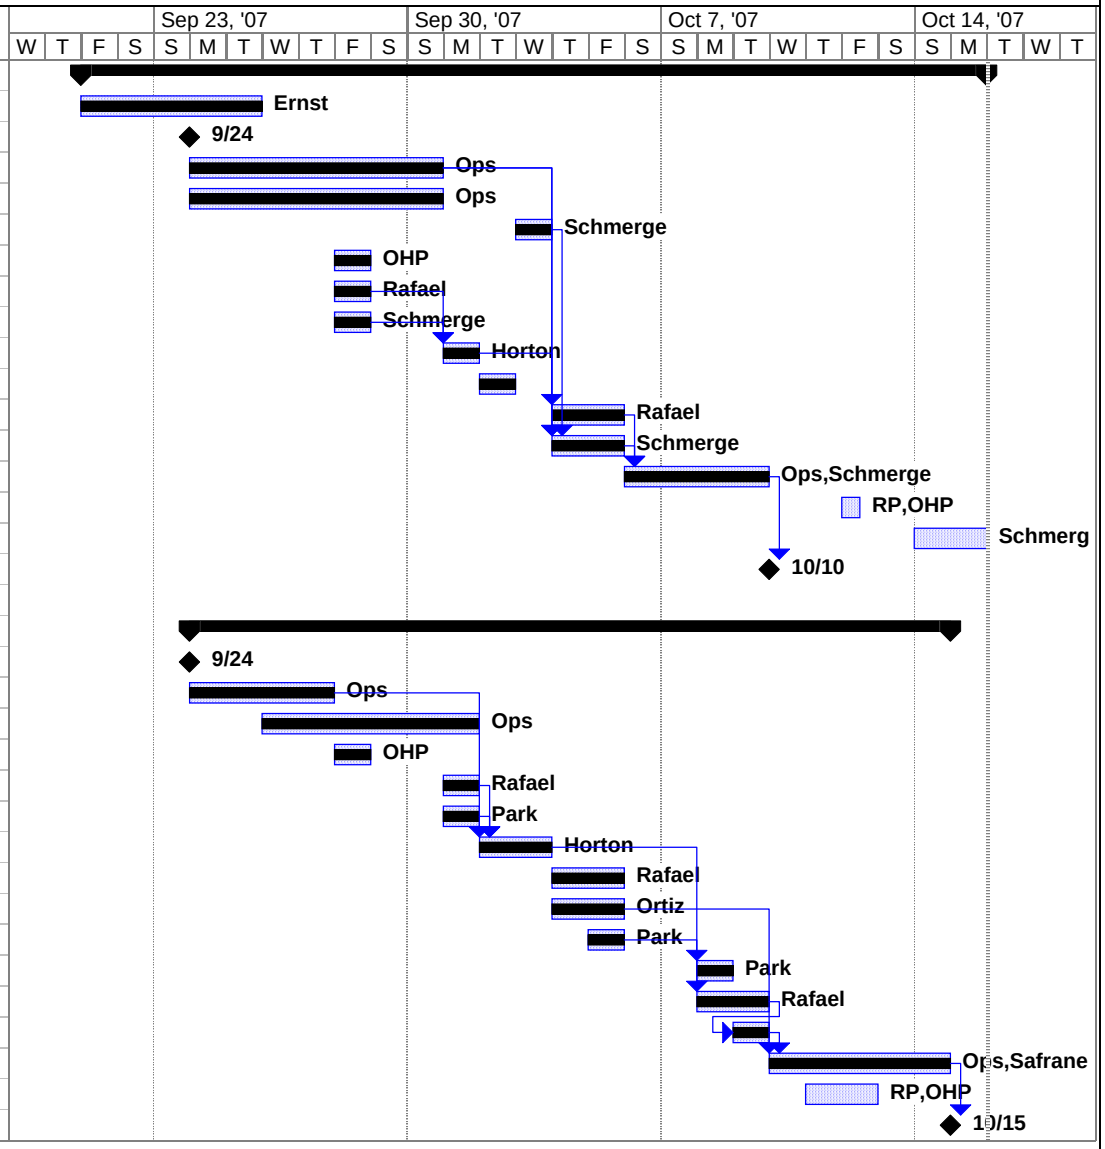ID		Task Name	Duration	Start
1		**LINAC & LTB**	**25 days**	**Fri 9/21/07**
2	✓	LCW ON	5 days	Fri 9/21/07
3	✓	Provide Linac BAS.	0 days	Mon 9/24/07
4	✓	BAS Checks.	7 days	Mon 9/24/07
5	✓	Pre-run Checks	7 days	Mon 9/24/07
6	✓	ACM checks (No Beam)	1 day	Wed 10/3/07
7	✓	BSOIC's Checks	1 day	Fri 9/28/07
8	✓	Prep PS's for PPS Cert.	1 day	Fri 9/28/07
9	✓	Prep RF for PPS Cert.	1 day	Fri 9/28/07
10	✓	PPS Certification	1 day	Mon 10/1/07
11	✓	Heat and smoke detectors for the	1 day	Tue 10/2/07
12	✓	PS's Itlk and power Checks	2 days	Thu 10/4/07
13	✓	RF Itlk and pwr checks	2 days	Thu 10/4/07
14	✓	Process Linac (Beam)	4 days	Sat 10/6/07
15		Rad survey Linac	0.5 days	Fri 10/12/07
16		ACM Cert. (with beam)	2 days	Sun 10/14/07
17	✓	BEAM to Booster	0 days	Wed 10/10/07
18				
19		**BOOSTER & BTS**	**21 days**	**Mon 9/24/07**
20	✓	Provide Booster BAS	0 days	Mon 9/24/07
21	✓	BAS Checks	4 days	Mon 9/24/07
22	✓	Pre-run Checks	6 days	Wed 9/26/07
23	✓	BCS (BSOIC's) Checks	1 day	Fri 9/28/07
24	✓	Prep PSs for PPS Cert.	1 day	Mon 10/1/07
25	✓	Prepare RF for PPS Cert	1 day	Mon 10/1/07
26	✓	PPS Certification	2 days	Tue 10/2/07
27	✓	Kicker Tests & Timing	2 days	Thu 10/4/07
28	✓	Heat & Smoke det test	2 days	Thu 10/4/07
29	✓	358 RF interlock Tests	1 day	Fri 10/5/07
30	✓	358 RF Processing	1 day	Mon 10/8/07
31	✓	PS's Itlk and Power Tests	2 days	Mon 10/8/07
32	✓	Controls Checks	1 day	Tue 10/9/07
33	✓	Establish Booster Beam	5 days	Wed 10/10/07
34		Injector Rad. Survey	2 days	Thu 10/11/07
35	✓	Beam to SPEAR	0 days	Mon 10/15/07
