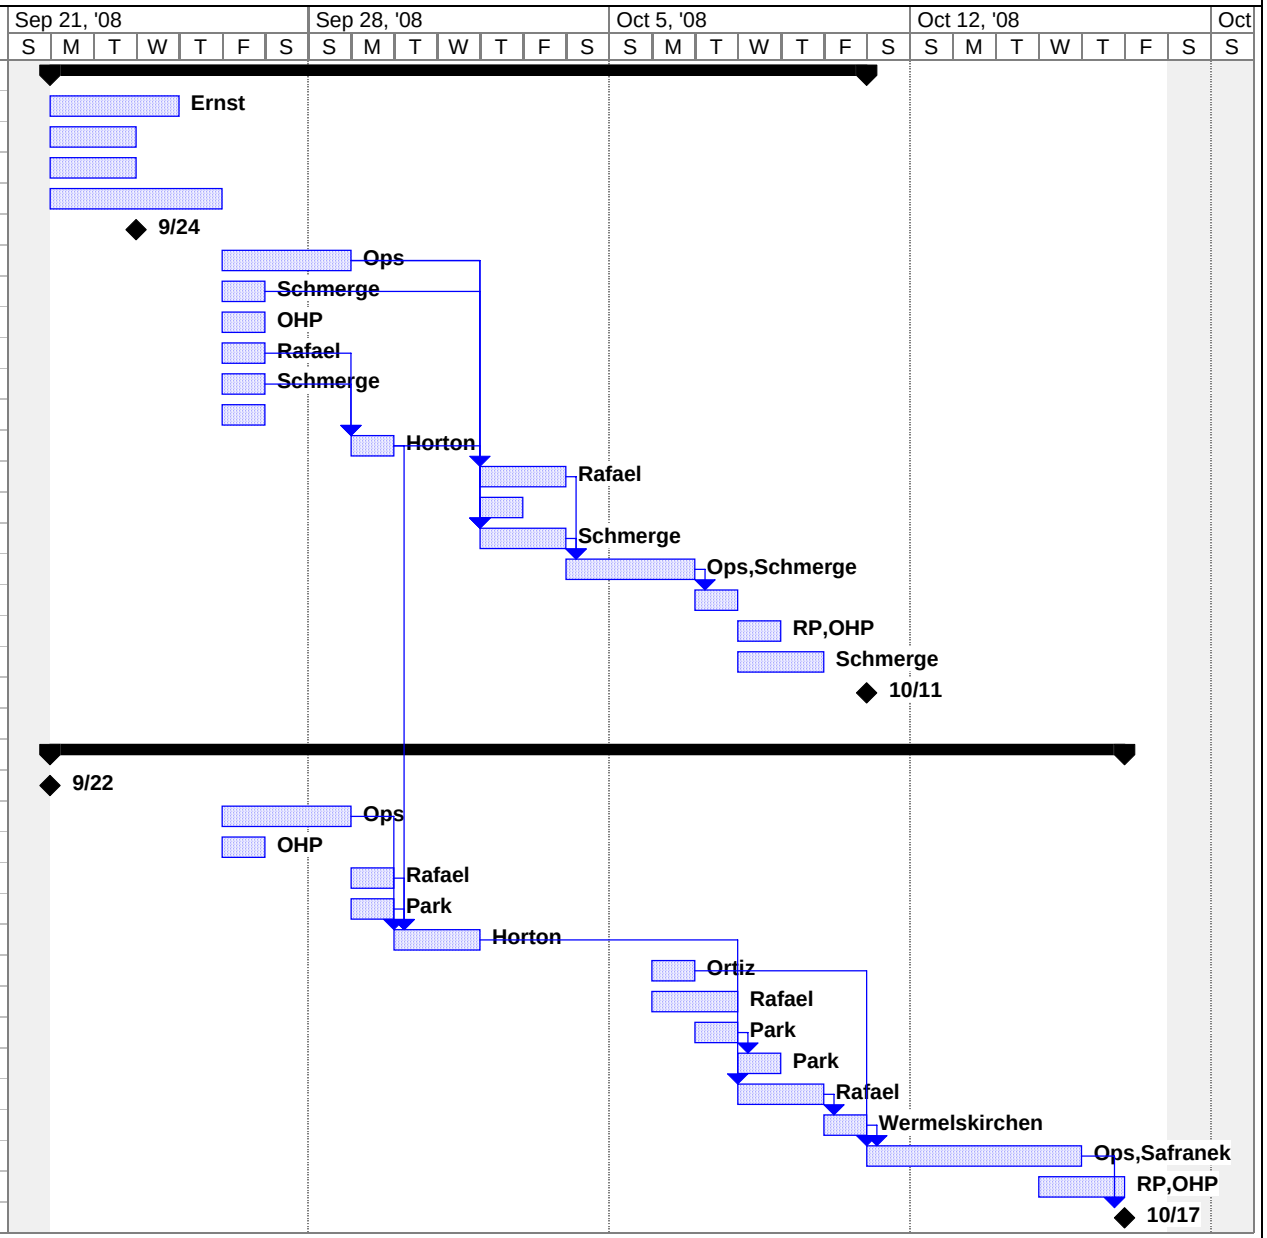ID	Task Name	Duration
1	**LINAC & LTB**	**19 days**
2	LCW ON	3 days
3	Control system ready	2 days
4	MPS ready for system tests	2 days
5	Other - MPS <- Alpha -I, Peaking	4 days
6	Provide Linac BAS.	0 days
7	BAS Checks and pre-run checks	3 days
8	ACM checks (No Beam)	1 day
9	BSOIC's Checks	1 day
10	Prep PS's for PPS Cert.	1 day
11	Prep RF for PPS Cert.	1 day
12	Heat and smoke detectors for the	1 day
13	PPS Certification	1 day
14	PS's Itlk and power Checks	2 days
15	Check Alpha-I MPS interlock	1 day
16	RF Itlk and pwr checks	2 days
17	Process Linac (Beam)	3 days
18	Tune Modulators	1 day
19	Rad survey Linac	1 day
20	ACM Cert. (with beam)	2 days
21	BEAM to Booster	0 days
22		
23	**BOOSTER & BTS**	**25 days**
24	Provide Booster BAS	0 days
25	BAS Checks and pre-run checks	3 days
26	BCS (BSOIC's) Checks	1 day
27	Prep PSs for PPS Cert.	1 day
28	Prepare RF for PPS Cert	1 day
29	PPS Certification	2 days
30	Heat & Smoke det test	1 day
31	Kicker Tests & Timing	2 days
32	358 RF interlock Tests	1 day
33	358 RF Processing	1 day
34	PS's Itlk and Power Tests	2 days
35	Controls Checks	1 day
36	Establish Booster Beam	5 days
37	Injector Rad. Survey	2 days
38	Beam to SPEAR(swing)	0 days
