Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float
S8_LCLS 2008 Install 4_19_07-mb_98					
S8X9_FH095	FEH Hutches Beneficial Occupancy	0		07/01/09	84
S8X9_FH070	Install FEH components - XT	60	07/02/09	10/16/09	84
S8X9_FH100	Terminate cable plant FEH	20	10/19/09	11/13/09	84
S8X9_FH110	Checkout Far Hall systems - XT	20	11/16/09	12/11/09	84
S8X9_FH125	TUN/FEH Install/Check Complete	0		12/11/09	84
S8Z2_SC090	Far Hall systems checks complete	0		12/11/09	84
S8Z2_SC100	PPS Certification process through FEH	15	12/14/09	01/05/10	84
S8Z3_CM180	System Ready for beam into FEH	0		01/05/10	84
S8Z3_CM190	Commission Hard X-rays through FEH	20	01/06/10	02/02/10	84
S8Z3_CM200	CD-4b Goals Achieved	0		02/02/10	84
MS1_PM040	CD4b - Start of Far Hall Ops - Project Complete	0		05/31/10*	0

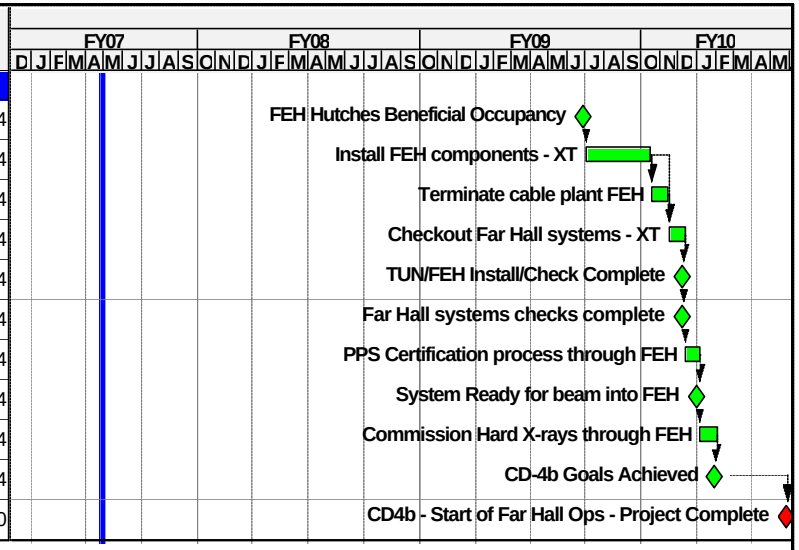

Start Date	07/19/06
Finish Date	05/31/10
Data Date	05/01/07
Run Date	06/21/07 15:59

Early Bar
Progress Bar
Critical Activity

CRFN
CD4b Critical Path

Sheet 1 of 1

LCLS PROJECT
Integrated Master Schedule
Installation Summary 2008
CD4b - Critical Path
0621_r1

© Primavera Systems, Inc.
