Activity ID	Activity Description	Early Start	Early Finish	Budgeted Cost
1 LCLS PROJECT - PED & CONSTRUCTION				
1.09 CONVENTIONAL FACILITIES				
1.09.01 System Management & Integration				
+ 1.09.01.01 Management				
		01FEB08	30JUL10	329,142
+ 1.09.01.02 CAM/CF Engineering				
		01FEB08	30SEP09	1,303,394
+ 1.09.01.03 Construction Management & AE Support				
		17OCT05A	30SEP09	4,113,342
1.09.03 Construction-T3 Conventional Facilities				
+ 1.09.03.03 BTH West				
		01FEB08	20MAR08	411,506
+ 1.09.03.04 Linac Facility Upgrade (LN)				
		21APR08	09JAN09	1,900,000
+ 1.09.03.05 Research Yard/B102,B211,B113 & Storage Trailers				
		19APR06A	30SEP08	985,357
+ 1.09.03.06 Pre-Purchase Equipment for Beam Path				
		01AUG06A	31JUL08	2,247,458
+ 1.09.03.07 SITEWORK, Earthwork, Site Utilities, & Survey				
		19JUL06A	30SEP09	14,043,632
+ 1.09.03.08 Beam Transport Hall (BTH)				
		02AUG06A	08AUG08	8,655,133
+ 1.09.03.09 Front End Enclosure (FEE)				
		09JUL07A	08AUG08	2,613,932
+ 1.09.03.10 Electron Beam Dump (EBD)				
		07MAR07A	08AUG08	2,507,554
+ 1.09.03.11 Near Experimental Hall (NEH)				
		11AUG06A	08AUG08	19,154,137
+ 1.09.03.12 Undulator Hall (UH)				
		02AUG06A	08AUG08	10,696,463
+ 1.09.03.13 X-Ray - Transport & Diagnostic Hall (XRTD)				
		09JUL07A	22AUG08	7,345,116
+ 1.09.03.14 Far Experimental Hall (FEH)				
		22AUG06A	01JUL09	15,890,643
+ 1.09.03.15 BTH Service Buildings 2.1, 2.2, and 2.3 (SB BTH)				
		16JUL07A	10APR08	3,882,300
+ 1.09.03.16 UH Service Building 3.1 (SB UH)				
		07FEB07A	07APR08	1,926,876
+ 1.09.03.17 FEH Access Tunnel Service Yard (SY FEH)				
		17DEC07A	06JUN08	1,492,036
+ 1.09.03.18 Central Utility Plant (CUP)				
		14NOV06A	16OCT08	5,592,372

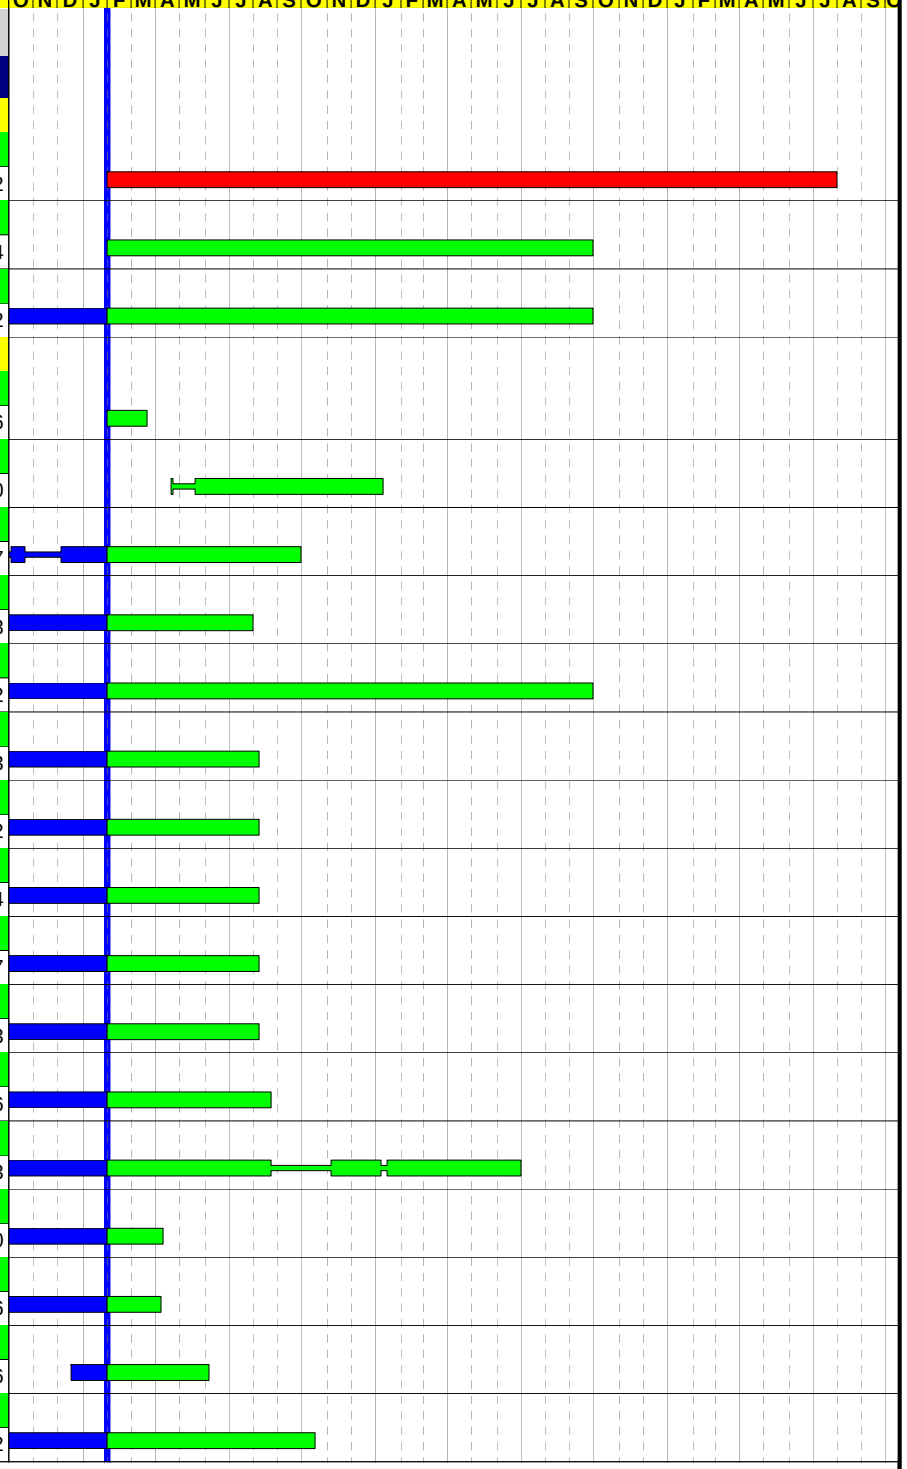
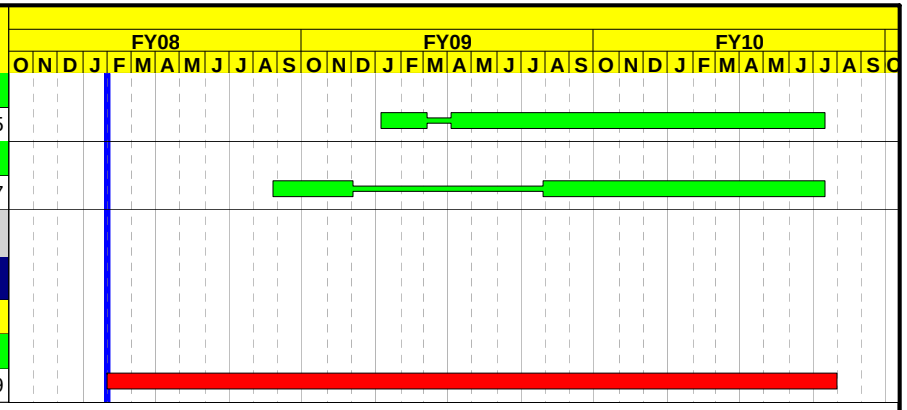
Activity ID	Activity Description	Early Start	Early Finish	Budgeted Cost
+ 1.09.03.19 SLAC Space Renovation for LCLS Ops				
		09JAN09	16JUL10	9,620,525
+ 1.09.03.20 Project Close Out - Conventional Facilities Syst				
		25AUG08	16JUL10	1,598,057
2 LCLS PROJECT - R&D, SPARES, COMMISSIONING				
2.09 Conventional Facility Commissioning				
2.09.03 Beam Path Project Commissioning				
+ 2.09.03.05 Beam Path Project Commissioning				
		01FEB08	30JUL10	1,473,649
