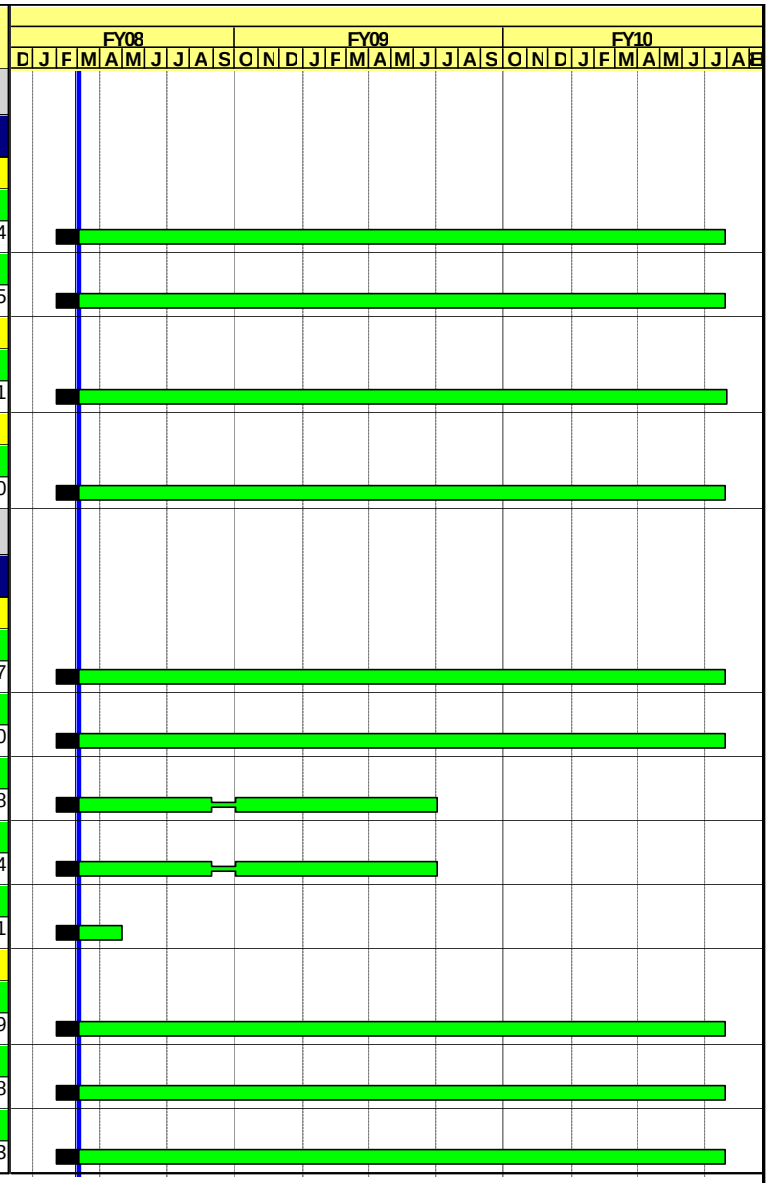Activity ID	Activity Description	Early Start	Early Finish	Budgeted Cost
1 LCLS PROJECT - PED & CONSTRUCTION				
1.01 LCLS PROJECT MGMT, PLANNING & ADMN (TEC)				
1.01.01 Environment, Safety & Health				
+ 1.01.01.01	Radiation Physics	02/01/08A	07/29/10	857,984
+ 1.01.01.02	ESH Management & Coordination	02/01/08A	07/29/10	542,155
1.01.02 Project Management				
+ 1.01.02.01	Project Management Office	02/01/08A	07/30/10	3,512,661
1.01.03 Technical Integration				
+ 1.01.03.03	System Integration	02/01/08A	07/29/10	242,390
2 LCLS PROJECT - R&D, SPARES, COMMISSIONING				
2.01 LCLS PROJECT MGMT, PLANNING & ADMN (OPC)				
2.01.01 LCLS Commissioning Mgmt & Physics Support				
+ 2.01.01.05	X-Ray Transport Physics	02/01/08A	07/29/10	417,977
+ 2.01.01.06	X-Ray Physics Commissioning	02/01/08A	07/29/10	248,300
+ 2.01.01.12	E-Beam Systems Commissioning Management	02/01/08A	07/02/09	370,868
+ 2.01.01.13	E-Beam Systems Physics Support	02/01/08A	07/02/09	786,914
+ 2.01.01.14	Laser Commissioning Management	02/01/08A	04/30/08	231,431
2.01.03 Project Mgmnt, Planning and Admn - M&S (OPC)				
+ 2.01.03.01	SLAC Project Office - General	02/01/08A	07/29/10	3,383,169
+ 2.01.03.02	SLAC Project Support	02/01/08A	07/29/10	2,264,828
+ 2.01.03.03	Project Mgmnt, Planning and Admn - M&S (OPC)	02/01/08A	07/29/10	1,560,273
