Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1 LCLS PROJECT - PED & CONSTRUCTION				
1.01 LCLS PROJECT MGMT, PLANNING & ADMN (TEC)				
PMLCLS_LOE	LCLS LOE Complete	0		03/31/09*
PM_LOE	PM LOE Complete	0		03/31/09
1.01.01 Environment, Safety & Health				
1.01.01.01 Radiation Physics				
PM110_0010	Radiation Physics - PED	107	05/02/05A	09/30/05A
PM110_0011	Radiation Physics- CONST FY06	242	10/03/05A	05/31/06A
PM110_0012	Radiation Physics- CONST FY06 Remainder	85*	06/01/06A	09/29/06
PM110_0015	Radiation Physics- CONST FY07	242	10/02/06	09/28/07
PM110_0020	Radiation Physics- CONST FY08	243	10/01/07	09/30/08
PM110_0025	Radiation Physics- CONST FY09	118	10/01/08	03/30/09
1.01.01.02 ESH Management & Coordination				
PM120_0020	ESH Management & Coordination - PED	107	05/02/05A	09/30/05A
PM120_0021	ESH Management & Coordination - (Hislop)	107	05/02/05A	09/30/05A
PM120_0024	Hazard Analysis Consulting - PED	107	05/02/05A	09/30/05A
PM120_0022	ESH Management & Coordination - FY06	242	10/03/05A	05/31/06A
PM120_0A25	Hazard Analysis Consulting - CONST A	242	10/03/05A	05/31/06A
PM120_0025	ESH Management & Coordination - FY06 Remainder	85*	06/01/06A	09/29/06
PM120_0027	ESH Management & Coordination - FY07	242	10/02/06	09/28/07
PM120_0028	ESH Management & Coordination - FY08	243	10/01/07	09/30/08
PM120_0029	ESH Management & Coordination - FY09	118	10/01/08	03/30/09
1.01.01.03 Seismic & Engineering Support				
PM120_0030	Seismic & Engineering - PED	107	05/02/05A	09/30/05A
PM120_0031	Seismic & Engineering - CONST FY06	845	10/03/05A	05/31/06A
PM120_0032	Seismic & Engineering - CONST FY06 Remainder	85*	06/01/06A	09/29/06
PM120_0033	Seismic & Engineering - CONST FY07-08	485	10/02/06	09/30/08
PM120_0034	Seismic & Engineering - CONST FY09	118	10/01/08	03/30/09

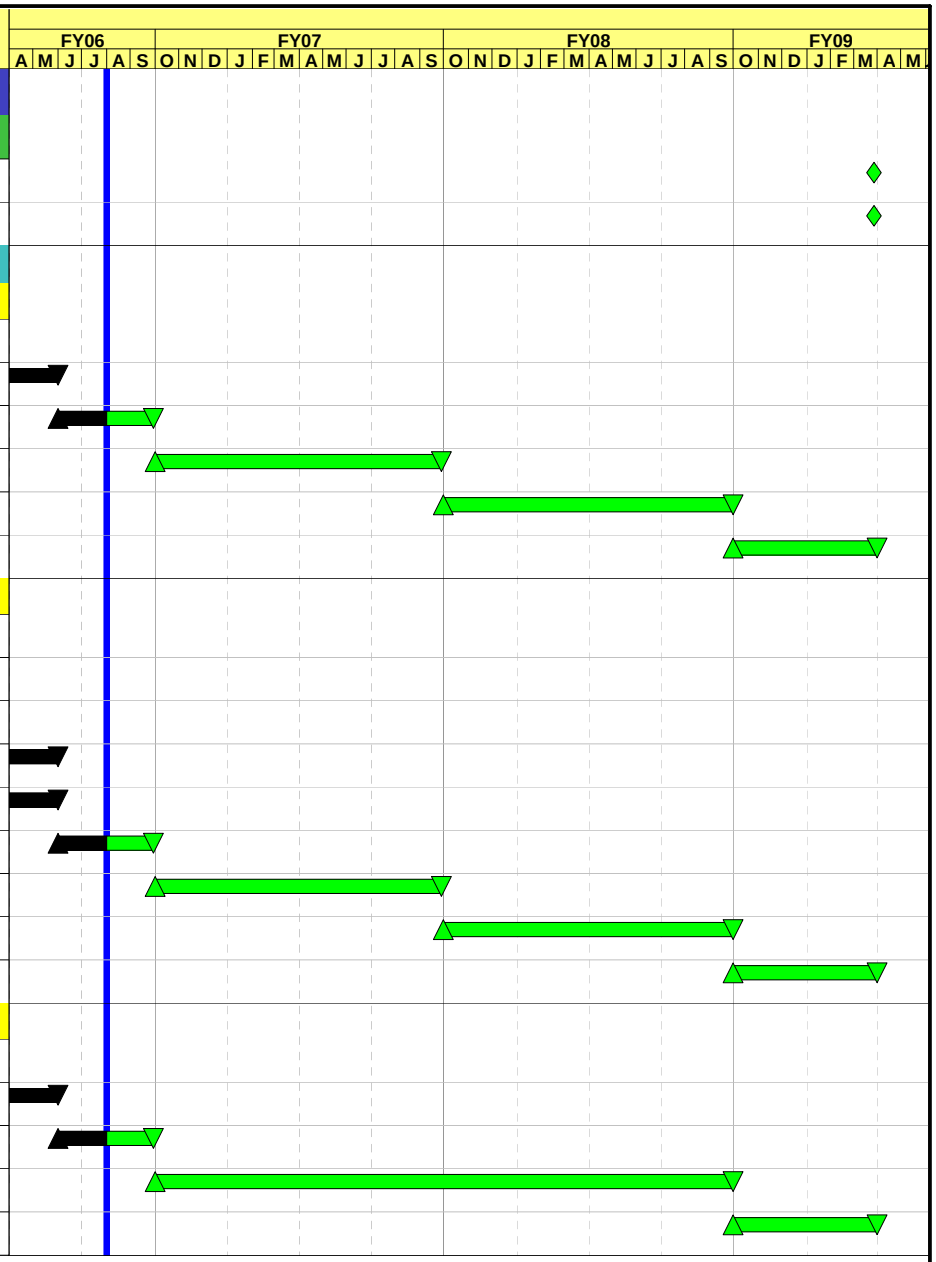

Start Date 06/01/01
Finish Date 04/01/09
Data Date 08/01/06

© Primavera Systems, Inc.

LCLS PROJECT
Integrated Master Schedule
Project Management

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1.01.02 Project Management				
1.01.02.01 Project Management Office				
1.01.02.01.01 Project Office - General				
PM211_0055	Administrative Support - CF & Proc - PED	64	05/02/05A	08/01/05A
PM211_0010	Project Director - PED	107	05/02/05A	09/30/05A
PM211_0020	Chief Engineer - PED	107	05/02/05A	09/30/05A
PM211_0025	E-Beam Systems Manager - PED	107	05/02/05A	09/30/05A
PM211_0030	Budget/Finance Officer - PED	107	05/02/05A	09/30/05A
PM211_0040	Administrative Support - SLAC 1 - PED	107	05/02/05A	09/30/05A
PM211_0050	Administrative Support - SLAC 2 - PED	107	05/02/05A	09/30/05A
PM211_0060	Photon System Manager - PED	107	05/02/05A	09/30/05A
PM211_0052	Administrative Support - CF & Proc - FY06	285*	08/02/05A	05/31/06A
PM211_0011	Project Director - CONST FY06	242	10/03/05A	05/31/06A
PM211_0021	Chief Engineer- CONST FY06	242	10/03/05A	05/31/06A
PM211_0027	E-Beam Systems Manager - FY06	242*	10/03/05A	05/31/06A
PM211_0031	Budget/Finance Officer - FY06	242*	10/03/05A	05/31/06A
PM211_0041	Administrative Support - SLAC 1 - FY06	242*	10/03/05A	05/31/06A
PM211_0051	Administrative Support - SLAC 2 - FY06	242*	10/03/05A	05/31/06A
PM211_0061	Photon System Manager - FY06	242*	10/03/05A	05/31/06A
PM211_0012	Project Director - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0022	Senior Project Mgrs - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0032	Budget/Finance Officer - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0053	Administrative Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0150	E-Beam Systems Manager - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0W53	Finance Administrative Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_160	Photon System Manager - FY06 Remainder	85*	06/01/06A	09/29/06
PM211_0013	Project Director - FY07	242	10/02/06	09/28/07
PM211_0023	Senior Project Mgrs - FY07	242	10/02/06	09/28/07
PM211_0033	Budget/Finance Officer - FY07	242	10/02/06	09/28/07
PM211_0054	Administrative Support - FY07	242	10/02/06	09/28/07
PM211_0151	E-Beam Systems Manager - FY07	242	10/02/06	09/28/07
PM211_0W54	Finance Administrative Support - FY07	242	10/02/06	09/28/07

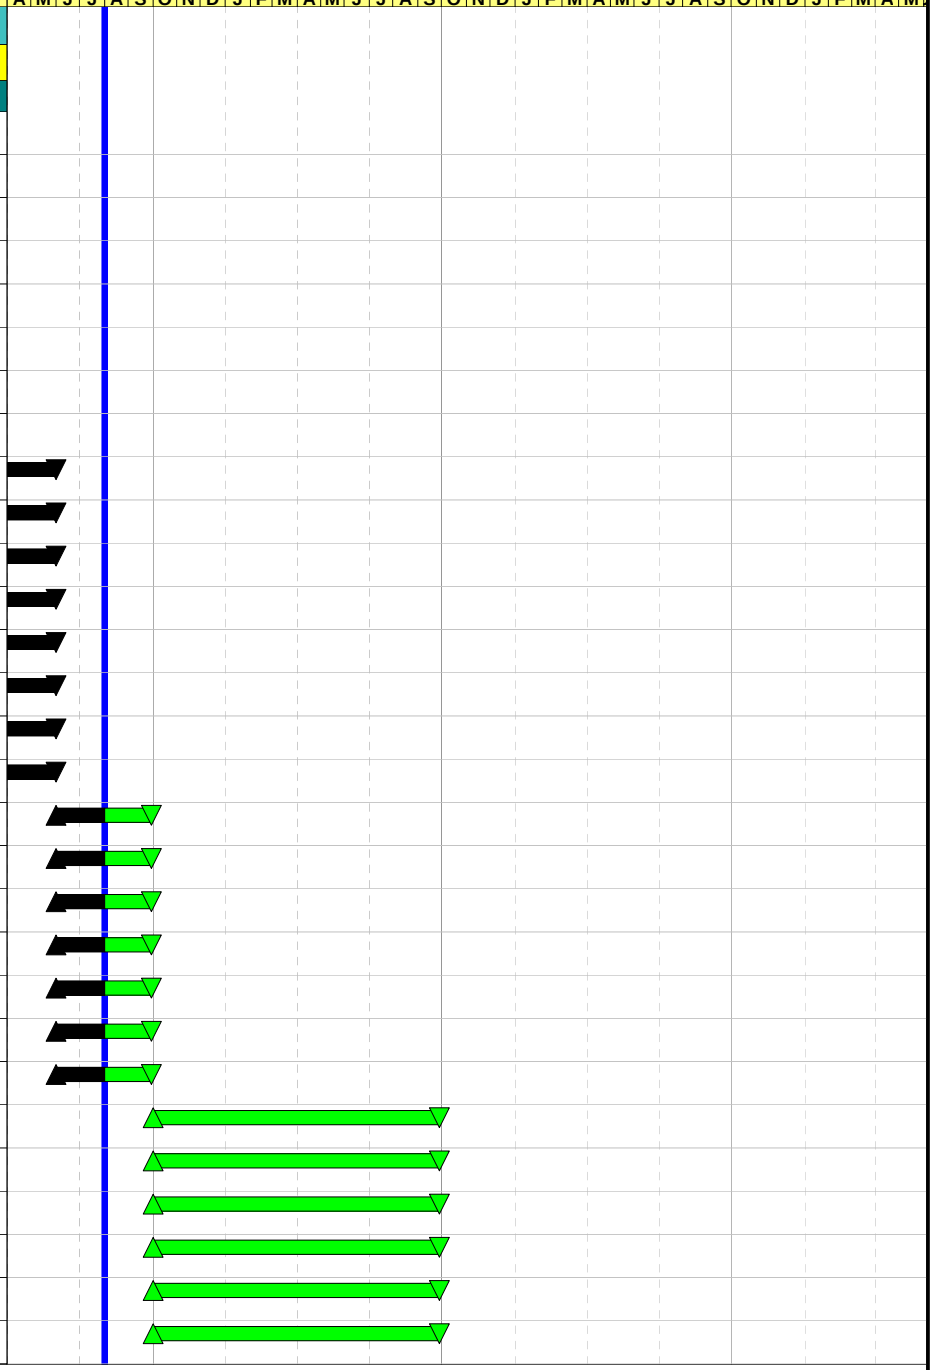

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1.01.02.01.01	**Project Office - General**			
PM211_161	Photon System Manager - FY07	242	10/02/06	09/28/07
PM211_0014	Project Director - FY08	243	10/01/07	09/30/08
PM211_0024	Senior Project Mgrs - FY08	243	10/01/07	09/30/08
PM211_0034	Budget/Finance Officer - FY08	243	10/01/07	09/30/08
PM211_0056	Administrative Support - FY08	243	10/01/07	09/30/08
PM211_0152	E-Beam Systems Manager - FY08	243	10/01/07	09/30/08
PM211_0W55	Finance Administrative Support - FY08	243	10/01/07	09/30/08
PM211_162	Photon System Manager - FY08	243	10/01/07	09/30/08
PM211_0015	Project Director- FY09	118	10/01/08	03/30/09
PM211_0026	Senior Project Mgrs - FY09	118	10/01/08	03/30/09
PM211_0035	Budget/Finance Officer - FY09	118	10/01/08	03/30/09
PM211_0057	Administrative Support - FY09	118	10/01/08	03/30/09
PM211_0153	E-Beam Systems Manager - FY09	118	10/01/08	03/30/09
PM211_0W57	Finance Administrative Support - FY09	118	10/01/08	03/30/09
PM211_163	Photon System Manager - FY09	118	10/01/08	03/30/09
1.01.02.01.02	**Project Support**			
PM212_0016	PMCS Support - Maintenance - PED	107	05/02/05A	09/30/05A
PM212_0020	Website Support - PED	107	05/02/05A	09/30/05A
PM212_0030	Relational Database Support - PED	107	05/02/05A	09/30/05A
PM212_0040	Procurement Support - PED	107	05/02/05A	09/30/05A
PM212_0050	QA/QC Support - PED	107	05/02/05A	09/30/05A
PM212_0060	Software Licenses - PED	107	05/02/05A	09/30/05A
PM212_0070	Computing Support - PED	107	05/02/05A	09/30/05A
PM212_0080	Recruiting/Relocation Support - PED	107	05/02/05A	09/30/05A
PM212_0061	Software Licenses - CONST	845	05/02/05A	05/31/06A
PM212_0021	Website Support - CONST	845	10/03/05A	05/31/06A
PM212_0031	Relational Database Support - CONST	845	10/03/05A	05/31/06A
PM212_0041	Procurement Support - CONST	845	10/03/05A	05/31/06A
PM212_0051	QA/QC Support - CONST	845	10/03/05A	05/31/06A
PM212_0071	Computing Support - CONST	845	10/03/05A	05/31/06A
PM212_0081	Recruiting/Relocation Support - CONST	845	10/03/05A	05/31/06A

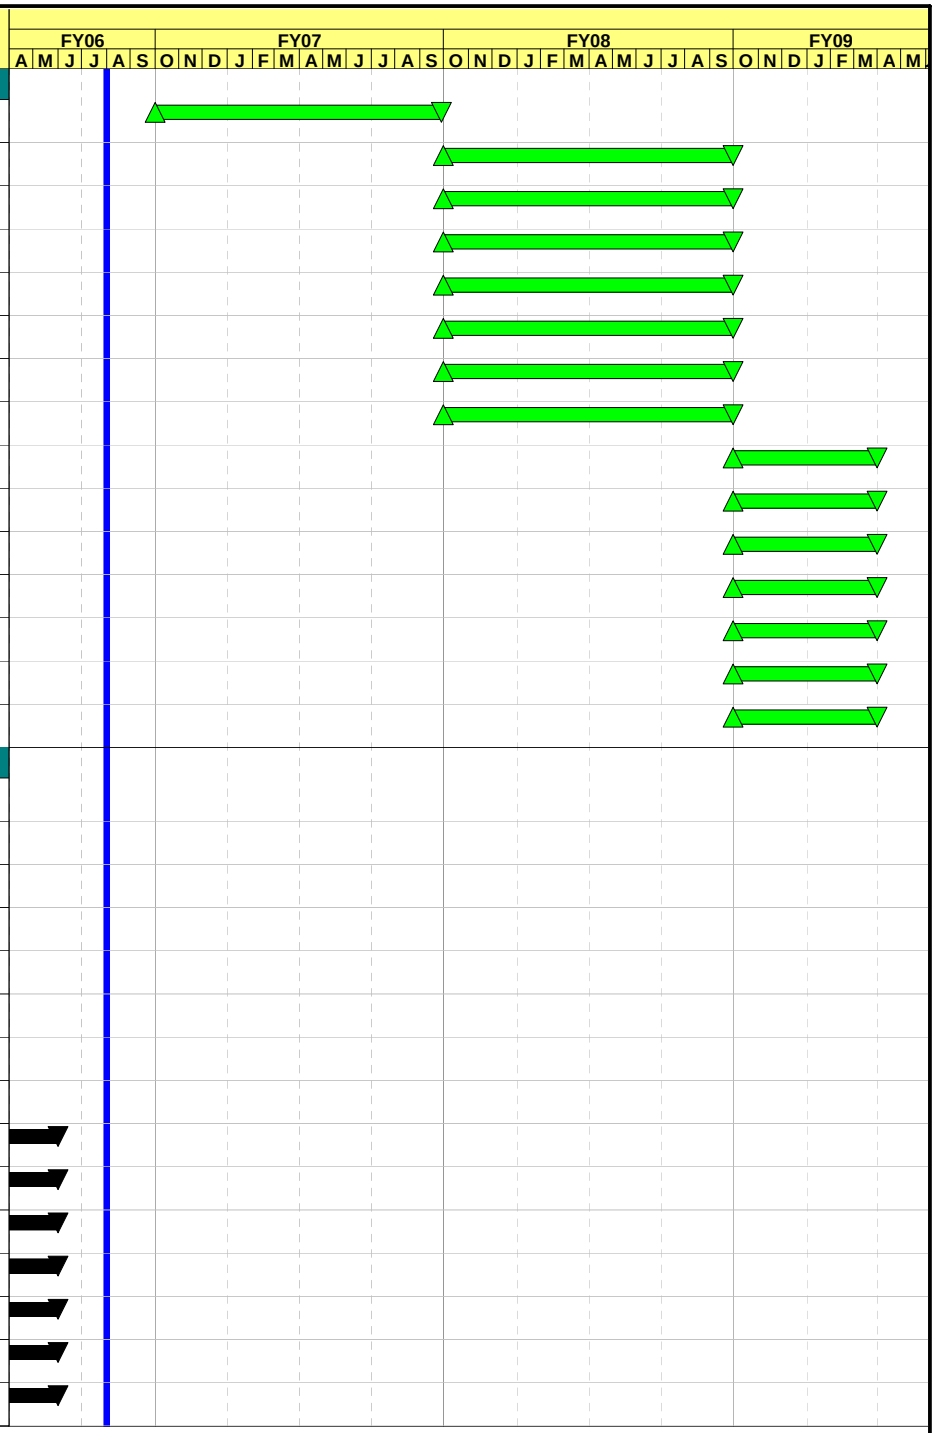

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1.01.02.01.02 Project Support				
PM212_0017	PMCS Support - Maintenance - FY06	242	10/13/05A	05/31/06A
PM212_0042	Additional Procurement Consulting Services	243	05/01/06A	05/31/06A
PM212_0052	QA/QC Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM212_0072	Computing Mgr Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM212_0090	Computing Res Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM212_0E17	PMCS Support - Maintenance - FY06 Rem	85*	06/01/06A	09/29/06
PM212_0044	Additional Procurement Consulting Serv Rem	327*	06/01/06A	09/28/07
PM212_0717	PMCS Support - Maintenance - (Oct06-May07)	158	10/02/06	05/31/07
PM212_0053	QA/QC Support - FY07	242	10/02/06	09/28/07
PM212_0073	Computing Mgr Support - FY07	242	10/02/06	09/28/07
PM212_0091	Computing Res Support - FY07	242	10/02/06	09/28/07
PM212_0022	AWARD: PMCS Support-FY07	1	10/03/06	10/03/06
PM212_A717	PMCS Support - Maintenance - (Jun07-Sep07)	84	06/01/07	09/28/07
PM212_0817	PMCS Support - Maintenance -(Oct07-Dec07)	53	10/01/07	12/14/07
PM212_0054	QA/QC Support - FY08	243	10/01/07	09/30/08
PM212_0074	Computing Mgr Support - FY08	243	10/01/07	09/30/08
PM212_0092	Computing Res Support - FY08	243	10/01/07	09/30/08
PM212_0023	AWARD: PMCS Support-FY08	1	10/02/07*	10/02/07
PM212_A817	PMCS Support - Maintenance -(Jan08-Jun08)	126	01/02/08	06/30/08
PM212_B817	PMCS Support - Maintenance -(Jul08-Sep08)	64	07/01/08	09/30/08
PM212_0024	AWARD: PMCS Support-FY09	1	10/01/08*	10/01/08
PM212_0055	QA/QC Support - FY09	118	10/01/08	03/30/09
PM212_0075	Computing Mgr Support - FY09	118	10/01/08	03/30/09
PM212_0093	Computing Res Support - FY09	118	10/01/08	03/30/09
PM212_0917	PMCS Support - Maintenance - FY09	118	10/01/08	03/30/09
1.01.02.01.03 Project Office M&S				
PM210_0440	Physics Programmatic Travel (R&D)	107	05/02/05A	09/30/05A
PM210_0460	SAC/FAC Travel - PED	107	05/02/05A	09/30/05A
PM213_0010	SLAC Project Office M&S - PED	107	05/02/05A	09/30/05A
PM213_0020	Tele/Video Conferencing - PED	107	05/02/05A	09/30/05A
PM213_0030	Computer M&S - PED	107	05/02/05A	09/30/05A

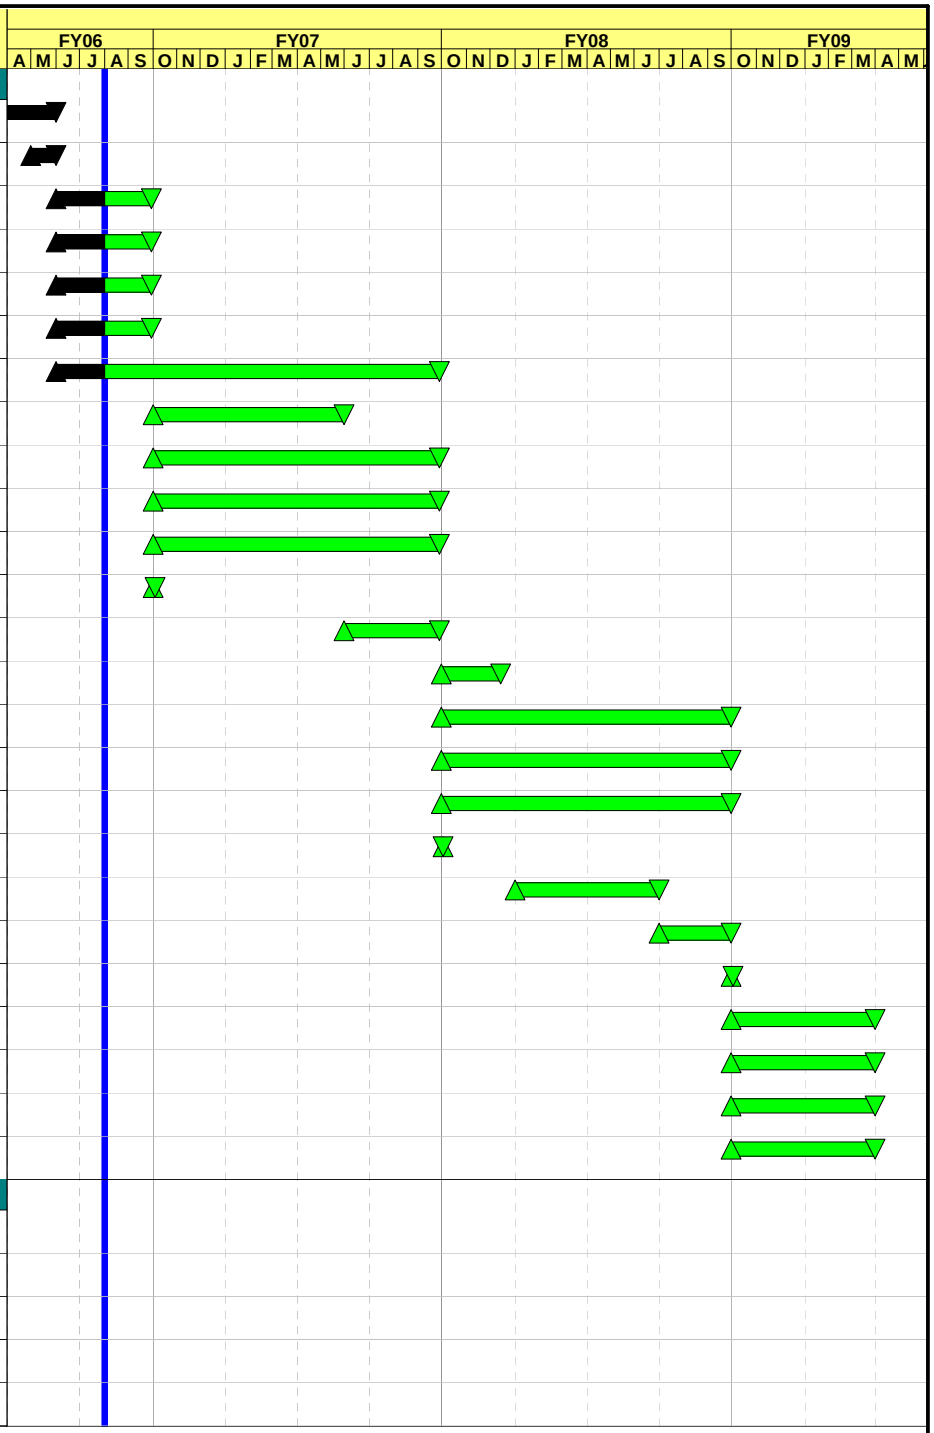

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1.01.02.01.03 Project Office M&S				
PM213_0040	Misc. Shipping/Storage Costs - PED	107	05/02/05A	09/30/05A
PM213_0050	Project Related Travel - PED	107	05/02/05A	09/30/05A
PM213_0055	Building Refurb/Remodeling @ SLAC - PED	107	05/02/05A	09/30/05A
PM213_0070	Review Committee Support - PED	107	05/02/05A	09/30/05A
PM213_0012	SLAC Project Office M&S - CONST FY06	201	10/02/05A	05/31/06A
PM213_0021	Tele/Video Conferencing - CONST	845	10/02/05A	05/31/06A
PM213_0031	Computer M&S - CONST	845	10/02/05A	05/31/06A
PM213_0041	Misc. Shipping/Storage Costs CONST	845	10/02/05A	05/31/06A
PM213_0071	Review Committee Support - CONST	845	10/02/05A	05/31/06A
PM213_0011	SLAC Project Office M&S - CONST	41	10/03/05A	11/30/05A
PM213_0051	Project Related Travel - CONST	845	10/03/05A	05/31/06A
PM213_0060	Building Refurb/Remodeling @ SLAC - CONST	845	10/03/05A	05/31/06A
PM213_0013	SLAC Project Office M&S	603	03/03/06A	05/31/06A
PM213_0014	SLAC Project Office Consumables- FY06	85*	06/01/06A	09/29/06
PM213_0052	Project Related Travel/ Shipping - FY06	85*	06/01/06A	09/29/06
PM213_0061	Software Licenses - CONST Remainder	581	06/01/06A	12/16/08
PM213_0A14	SLAC Project Office Consumables- FY07	242	10/02/06*	09/28/07
PM213_0A52	Project Related Travel/ Shipping - FY07	242	10/02/06	09/28/07
PM213_0016	SLAC Project Office Consumables- FY08	243	10/01/07*	09/30/08
PM213_0053	Project Related Travel/ Shipping - FY08	243	10/01/07	09/30/08
PM213_0017	SLAC Project Office Consumables- FY09	118	10/01/08*	03/30/09
PM213_0054	Project Related Travel/ Shipping - FY09	118	10/01/08	03/30/09
1.01.02.01.04 SSRL Physics Support				
PM213_0100	SSRL Physics Support	31	05/02/05A	06/14/05A
PM213_0105	SSRL Physics Support	53	10/03/05A	12/16/05A
1.01.03 Technical Integration				
1.01.03.02 Global Alignment Coordination				
PM100_0000	Global Laser Coordination - PED	107	05/02/05A	09/30/05A
PM300_0050	Global Alignment Coordination - PED	107	05/02/05A	09/30/05A
PM300_0160	Procure Surface Network Components	120	10/03/05A	04/07/06A
PM300_0051	Global Alignment Coordination - CONST	845	10/03/05A	05/31/06A
PM300_0150	Surface Network Oversight and Integration	484	10/03/05A	05/31/06A

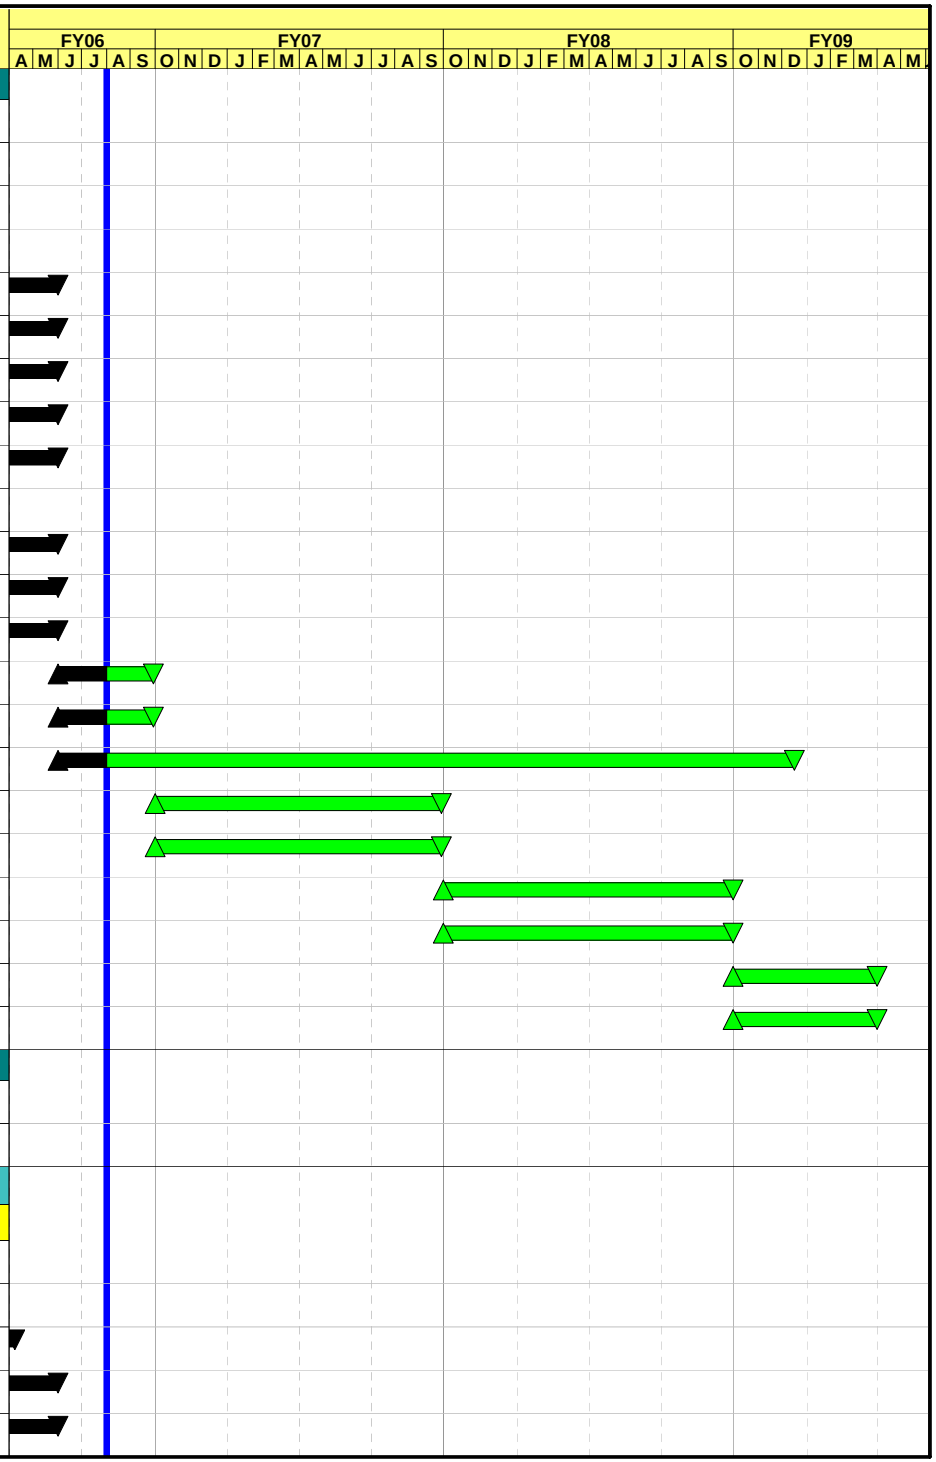

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1.01.03.02 Global Alignment Coordination				
PM300_0170	Install and Measure Surface Network	484	10/03/05A	05/31/06A
PM100_0006	Global Laser Coordination - FY06 Remainder	85*	06/01/06A	09/29/06
PM100_0005	Global Laser Coordination - FY06	157		05/31/06A
1.01.03.03 System Integration				
PM300_0060	Installation Coordination - PED	107	05/02/05A	09/30/05A
PM300_0062	Design Supervisor - PED	107	05/02/05A	09/30/05A
PM300_0061	Installation Coordination - CONST	845	10/03/05A	05/31/06A
PM300_0063	Design Supervisor - CONST	845	10/03/05A	05/31/06A
PM300_0064	Installation Coordination - FY06 Rem	85*	06/01/06A	09/29/06
PM300_0074	Design Supervisor - FY06 Remainder	85*	06/01/06A	09/29/06
PM300_0065	Installation Coordination - FY07	242	10/02/06	09/28/07
PM300_0075	Design Supervisor - FY07	242	10/02/06*	09/28/07
PM300_0066	Installation Coordination - FY08	243	10/01/07*	09/30/08
PM300_0067	Installation Coordination - FY09	118	10/01/08*	03/30/09
1.01.03.06 Technical Requirements/Parameters				
PM210_0291	Define Technical Requirements/Parameters(PED)	107	05/02/05A	09/30/05A
PM210_0292	Define Technical Requirements/Parameters(LLP)	242	10/03/05A	05/31/06A
PM210_0293	Define Technical Requirements/Parameters(CON)	85*	06/01/06A	09/29/06
1.01.04 Education Support				
1.01.04.01 Education/Outreach Travel				
PM400_0030	Education Support - PED	107	05/02/05A	09/30/05A
PM400_0031	Education Support - CONST	845	10/03/05A	05/31/06A
1.01.04.02 Education/Outreach M&S				
PM400_0040	Education/Outreach M&S - PED	107	05/02/05A	09/30/05A
PM400_0041	Education/Outreach M&S - CONST	845	10/03/05A	05/31/06A

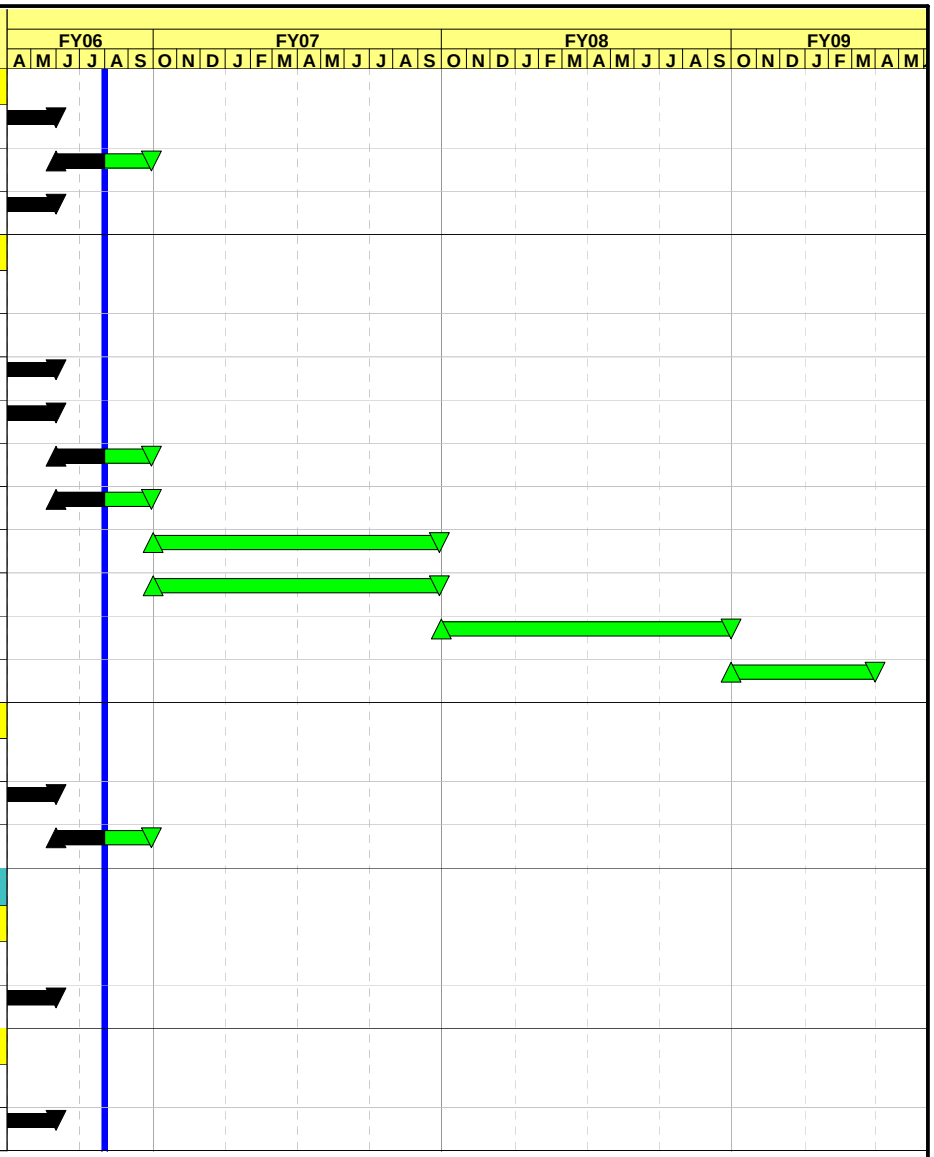

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2 LCLS PROJECT - R&D, SPARES, COMMISSIONING				
2.01 LCLS PROJECT MGMT, PLANNING & ADMN (OPC)				
2.01.01 Physics Support (OPC)				
2.01.01.01 LCLS Commissioning Management				
PM210_0290	Physics Group Leader	107	05/02/05A	09/30/05A
PM210_0360	Physics Group Leader	845	10/03/05A	05/31/06A
PM210_0365	Additional Physics Support	129	05/01/06A	05/31/06A
PM210_0361	Physics Group Leader Remainder	688*	06/01/06A	03/30/09
2.01.01.02 Injector Physics				
PM210_0300	Injector Physicists	107	05/02/05A	09/30/05A
PM210_0375	Laser & RF Gun Physics Development	107	05/02/05A	09/30/05A
PM210_0370	Injector Physicists	242	10/03/05A	05/31/06A
PM210_0385	Laser & RF Gun Physics Development	845	10/03/05A	05/31/06A
PM210_C372	Injector Physicists ETC2	43*	08/01/06A	09/29/06
PM210_A386	Laser & RF Gun Physics Dev ETC2	646*	08/01/06A	03/30/09
PM210_0371	Injector Physicists-Apr 07	136	10/02/06	04/30/07
PM210_A372	Injector Physicists- May07-Jul08	307	05/01/07	07/31/08
PM210_B372	Injector Physicists- Aug08-Mar09	160	08/01/08	03/30/09
2.01.01.03 Linac Physics				
PM210_0310	Linac Physicists	107	05/02/05A	09/30/05A
PM210_0380	Linac Physicists	242	10/03/05A	05/31/06A
PM210_0383	Linac Physicists FY06 Remainder	85*	06/01/06A	09/29/06
PM210_0381	Linac Physicists	603	10/02/06	03/30/09
2.01.01.04 Undulator Physics				
PM210_0320	Undulator Physicists	107	05/02/05A	09/30/05A
PM210_0390	Undulator Physicists	242	10/03/05A	05/31/06A
PM210_0393	Undulator Physicists FY06 Remainder	85*	06/01/06A	09/29/06
PM210_0391	Undulator Physicists	603	10/02/06	03/30/09
2.01.01.05 X-Ray Transport Physics				
PM210_0330	X-Ray Transport Physicists	107	05/02/05A	09/30/05A
PM210_0400	X-Ray Transport Physicists	845	10/03/05A	05/31/06A
PM210_0401	X-Ray Transport Physicists Remainder	688*	06/01/06A	03/30/09

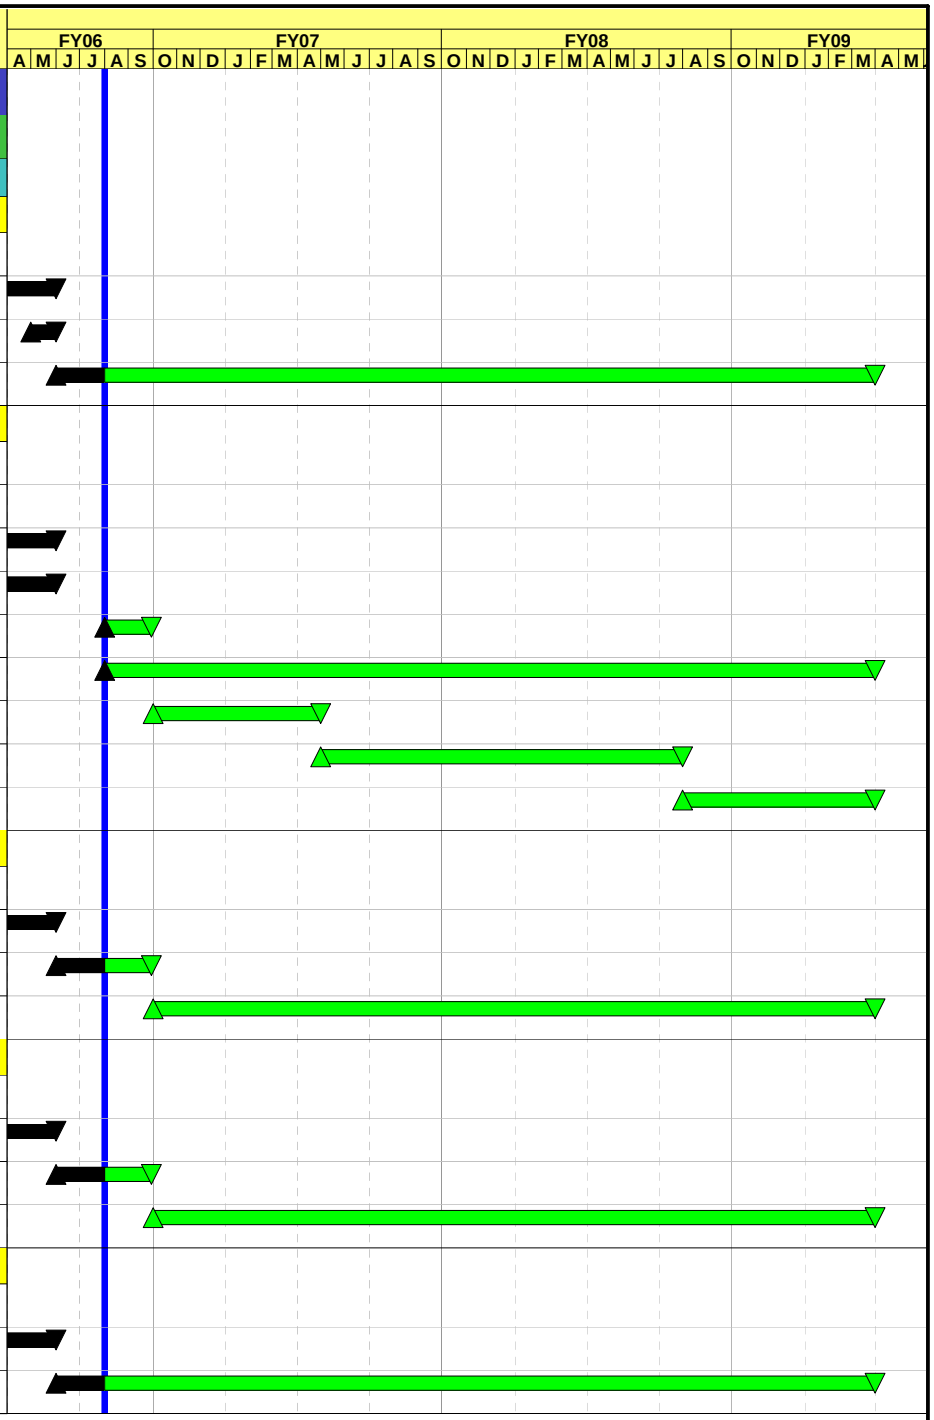

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2.01.01.06 X-Ray Physics Commissioning				
PM210_0340	X-Ray Endstation Physicists	107	05/02/05A	09/30/05A
PM210_0410	X-Ray Endstation Physicists	845	10/03/05A	05/31/06A
PM210_0411	X-Ray Endstation Physicists Remainder	602	10/03/06	03/30/09
2.01.01.07 Conventional Facilities Physics				
PM210_0350	Conventional Facility Physicists	107	05/02/05A	09/30/05A
PM210_0420	Conventional Facility Physicists	242	10/03/05A	05/31/06A
PM210_0423	Conventional Fac Physicists FY06 Remain	85*	06/01/06A	09/29/06
PM210_0421	Conventional Facility Physicists-Apr07	136	10/02/06	04/30/07
PM210_A421	Conventional Facility Physicists May07-Jul08	307	05/01/07	07/31/08
PM210_B421	Conventional Facility Physicists Aug08-Mar09	160	08/01/08	03/30/09
2.01.01.08 Consulting Physics (Collaboration)				
PM210_0240	Consulting Collaboration Physicists	107	05/02/05A	09/30/05A
PM210_0430	Consulting Collaboration Physicists	845	10/03/05A	05/31/06A
PM210_0431	Consulting Collaboration Physicists Rem	688*	06/01/06A	03/30/09
2.01.01.09 Consulting Physics (SLAC)				
PM210_0130	Consulting SLAC Physicists	107	05/02/05A	09/30/05A
PM210_0270	Consulting SLAC Physicists	845	10/03/05A	05/31/06A
PM210_0271	Planning Experiment Startup	94	11/01/05A	03/31/06A
PM210_A366	Physics Support FY06	65*	08/01/06A	10/31/06
PM210_B272	Consulting SLAC Physicists FY06-Mar07 (2)	158*	08/01/06A	03/30/07
PM210_0367	Physics Support FY07	242	11/01/06*	10/30/07
PM210_A272	Consulting SLAC Physicists Apr07-Sep07	127	04/02/07*	09/28/07
PM210_0273	Consulting SLAC Physicists FY08	243	10/01/07*	09/30/08
PM210_0368	Physics Support FY08	243	10/31/07*	10/30/08
PM210_0274	Consulting SLAC Physicists FY09	118	10/01/08*	03/30/09
2.01.01.10 Global Controls Physics Liaison				
PM210_0250	Global Controls Physicists Liaison	107	05/02/05A	09/30/05A
PM210_0280	Global Controls Physicists Liaison	242	10/03/05A	05/31/06A
PM210_0281	Global Controls Phys Liaison Rem	688*	06/01/06A	03/30/09
2.01.02 R&D Studies & Prototyping				
2.01.02.01 R&D Studies & Prototyping				
PM210_0260	R&D Studies & Prototyping	107	05/02/05A	09/30/05A

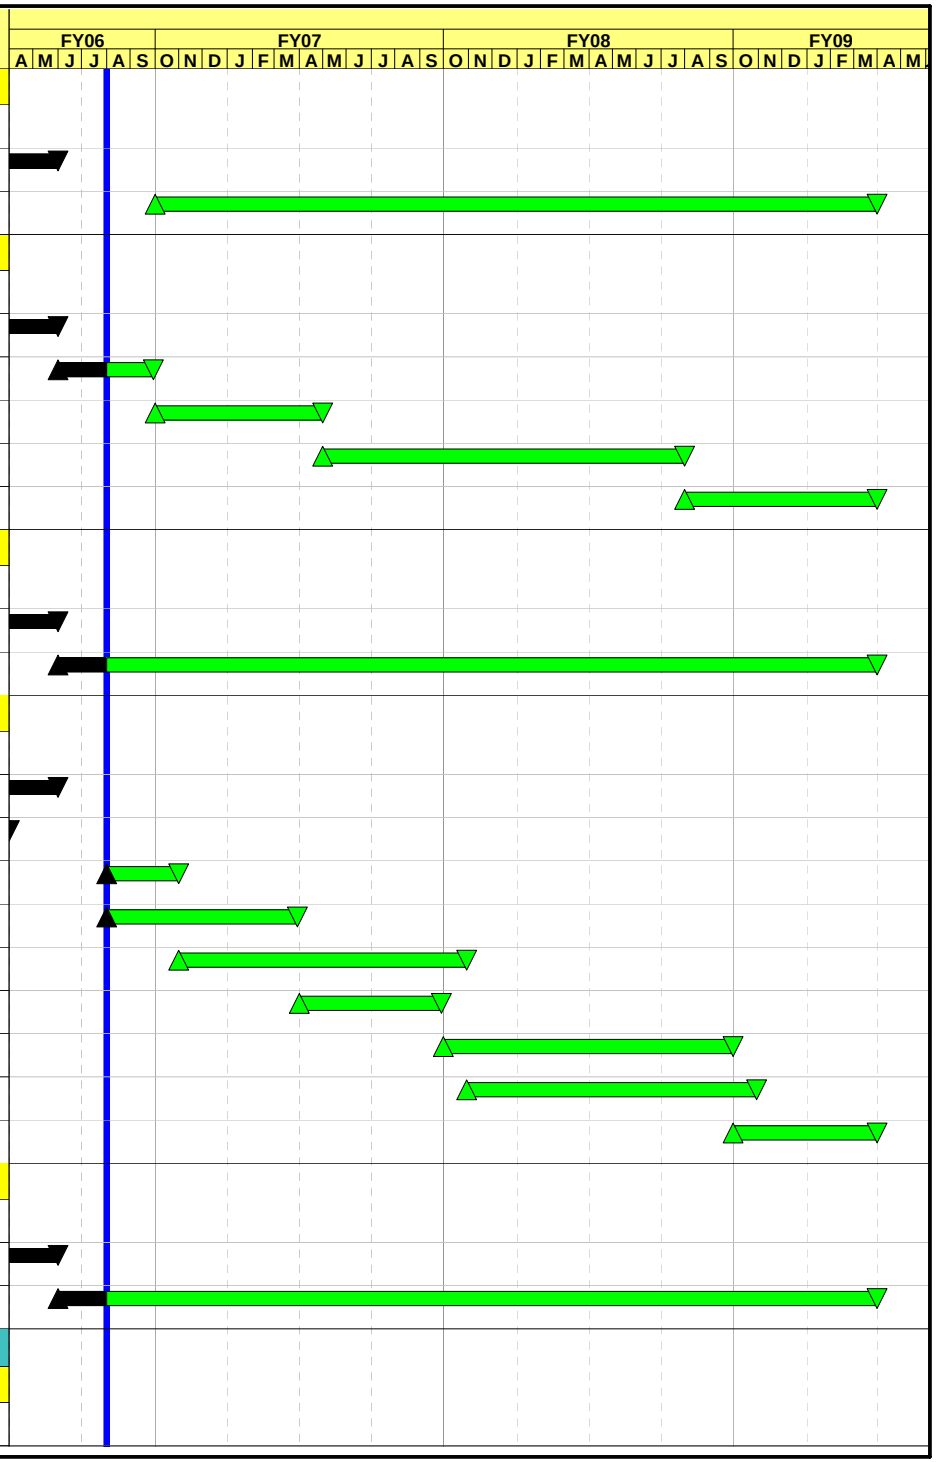

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2.01.02.01 R&D Studies & Prototyping				
PM210_0265	Low Level Applications R&D	107	05/02/05A	09/30/05A
PM210_0275	Low Level Applications Commissioning	845	10/03/05A	05/31/06A
2.01.03 Project Mgmnt, Planning and Admn - M&S (OPC)				
2.01.03.01 SLAC Project Office - General				
PM213_0000	Project Director - R&D	107	05/02/05A	09/30/05A
PM213_0005	Chief Engineer - R&D	107	05/02/05A	09/30/05A
PM213_0007	E-Beam Systems Oversight Manager - R&D	107	05/02/05A	09/30/05A
PM213_0015	Budget/Finance Officer - R&D	107	05/02/05A	09/30/05A
PM213_0025	Administrative Support - SLAC 1 - R&D	107	05/02/05A	09/30/05A
PM213_0200	Administrative Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0220	Budget/Finance Officer - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0240	Project Director - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0260	Senior Project Mgrs - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0280	E-Beam Systems Manager - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0300	Photon System Manager - FY06 Remainder	85*	06/01/06A	09/29/06
PM213_0205	Administrative Support - FY07	242	10/02/06	09/28/07
PM213_0225	Budget/Finance Officer - FY07	242	10/02/06	09/28/07
PM213_0245	Project Director - FY07	242	10/02/06	09/28/07
PM213_0265	Senior Project Mgrs - FY07	242	10/02/06	09/28/07
PM213_0285	E-Beam Systems Manager - FY07	242	10/02/06	09/28/07
PM213_0305	Photon System Manager - FY07	242	10/02/06	09/28/07
PM301_7000	Global Laser Coordination - FY07	242*	10/02/06	09/28/07
PM213_0210	Administrative Support - FY08	243	10/01/07	09/30/08
PM213_0230	Budget/Finance Officer - FY08	243	10/01/07	09/30/08
PM213_0250	Project Director - FY08	243	10/01/07	09/30/08
PM213_0270	Senior Project Mgrs - FY08	243	10/01/07	09/30/08
PM213_0290	E-Beam Systems Manager - FY08	243	10/01/07	09/30/08
PM213_0310	Photon System Manager - FY08	243	10/01/07	09/30/08
PM301_8000	Global Laser Coordination - FY08	243*	10/01/07	09/30/08
PM213_0215	Administrative Support - FY09	118	10/01/08	03/30/09
PM213_0235	Budget/Finance Officer - FY09	118	10/01/08	03/30/09

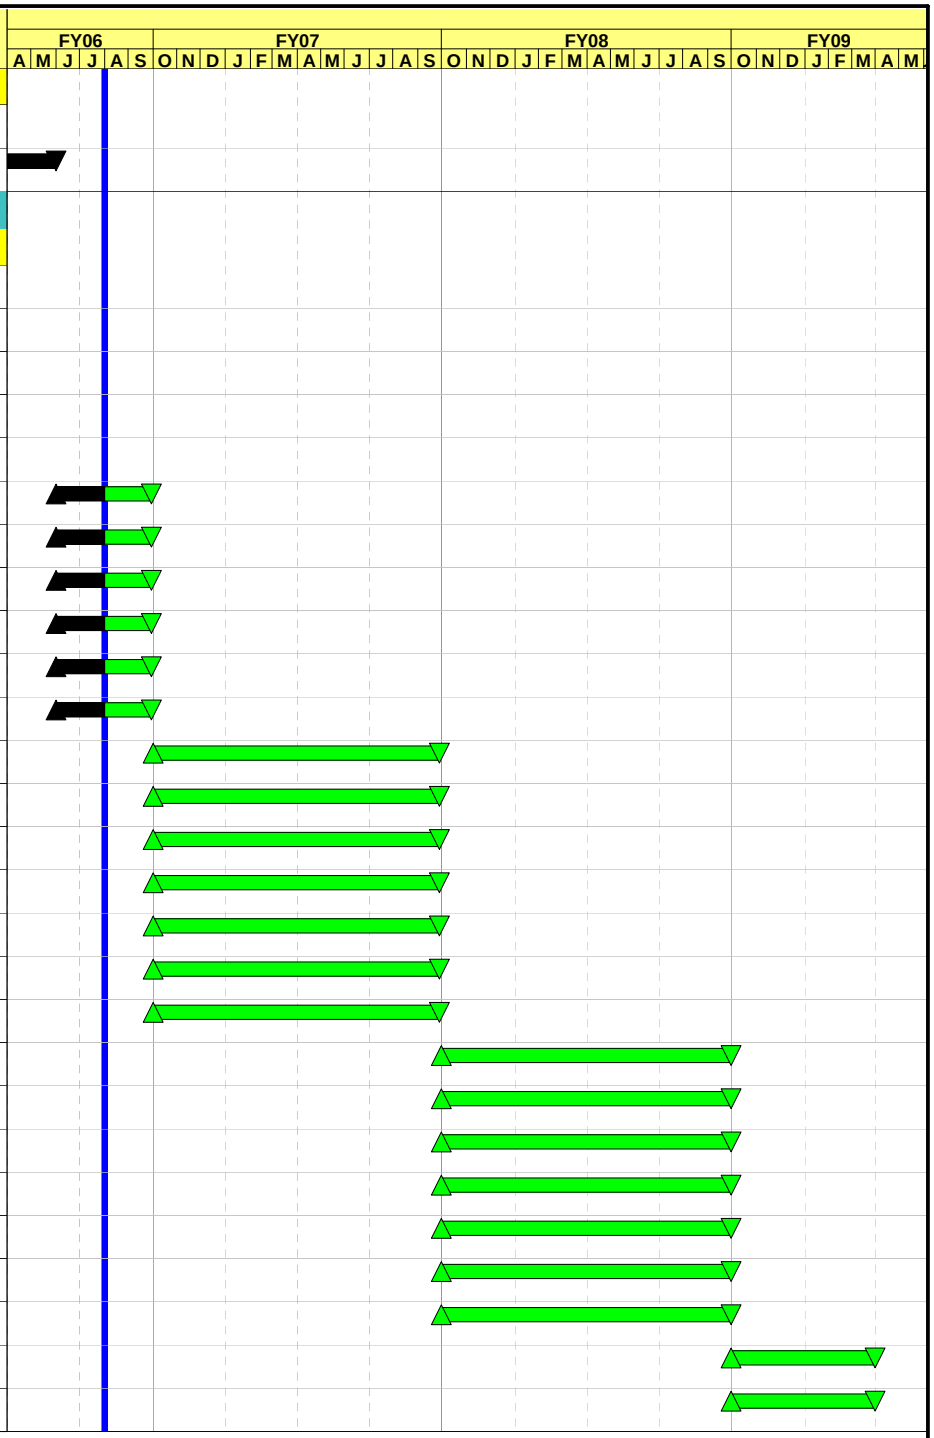

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2.01.03.01 SLAC Project Office - General				
PM213_0255	Project Director- FY09	118	10/01/08	03/30/09
PM213_0275	Senior Project Mgrs - FY09	118	10/01/08	03/30/09
PM213_0295	E-Beam Systems Manager - FY09	118	10/01/08	03/30/09
PM213_0315	Photon System Manager - FY09	118	10/01/08	03/30/09
PM301_9000	Global Laser Coordination - FY09	118*	10/01/08	03/30/09
2.01.03.02 SLAC Project Support				
PM210_0995	PMCS Support - Maintenance - FY06	107	05/01/06A	05/31/06A
PM210_0996	PMCS Support - Maintenance - FY06 Rem	85*	06/01/06A	09/29/06
PM212_0152	QA/QC Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM212_0172	Computing Mgr Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM212_0190	Computing Res Support - FY06 Remainder	85*	06/01/06A	09/29/06
PM300_0166	Installation Coordination - FY08	243*	06/01/06A	05/31/07
PM212_0153	QA/QC Support - FY07	242	10/02/06*	09/28/07
PM212_0173	Computing Mgr Support - FY07	242	10/02/06*	09/28/07
PM212_0191	Computing Res Support - FY07	242	10/02/06*	09/28/07
PM212_A022	AWARD: PMCS Support-FY07	1	10/03/06	10/03/06
PM210_1000	PMCS Support - Maintenance - (Oct06-May07)	158	10/03/06	06/01/07
PM300_0167	Installation Coordination - FY09	118	06/01/07*	11/15/07
PM210_1A00	PMCS Support - Maintenance -(Jun07-Sep07)	84	06/04/07	10/01/07
PM212_0154	QA/QC Support - FY08	243	10/01/07*	09/30/08
PM212_0174	Computing Mgr Support - FY08	243	10/01/07*	09/30/08
PM212_0192	Computing Res Support - FY08	243	10/01/07*	09/30/08
PM212_A023	AWARD: PMCS Support-FY08	1	10/02/07*	10/02/07
PM210_1010	PMCS Support - Maintenance -(Oct-7-Dec07)	53	10/02/07	01/02/08
PM210_1A10	PMCS Support - Maintenance -(Jan08-Jun08)	126	01/03/08	07/01/08
PM210_1B10	PMCS Support - Maintenance -(Jul08-Sep08)	64	07/02/08	10/01/08
PM212_0155	QA/QC Support - FY09	118	10/01/08*	03/30/09
PM212_0175	Computing Mgr Support - FY09	118	10/01/08*	03/30/09
PM212_0193	Computing Res Support - FY09	118	10/01/08*	03/30/09
PM212_A024	AWARD: PMCS Support-FY09	1	10/02/08*	10/02/08
PM210_1020	PMCS Support - Maintenance - FY09	118	10/02/08	03/31/09

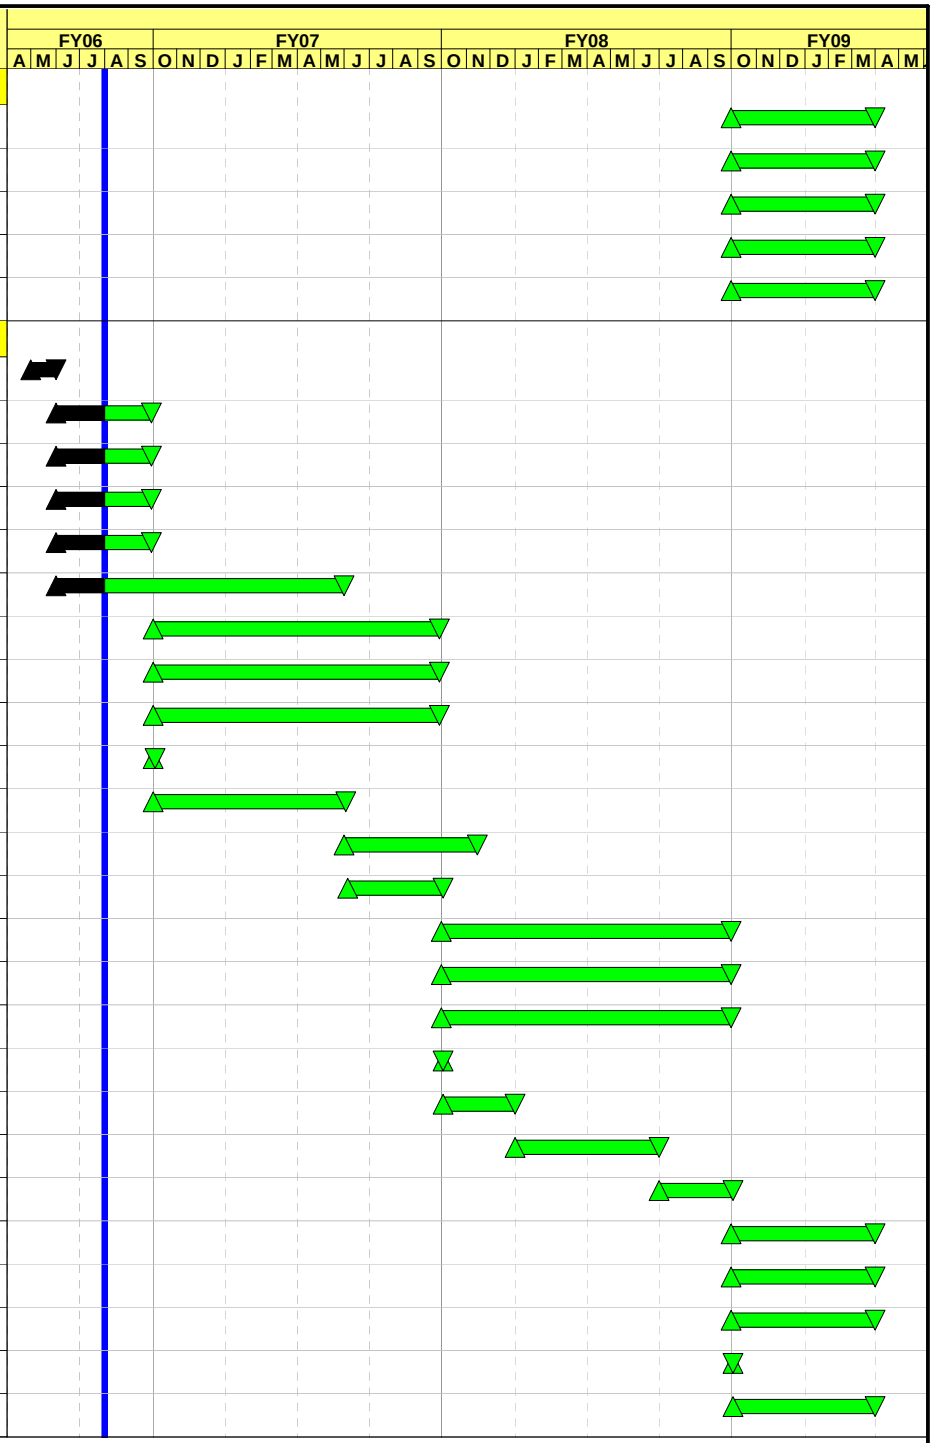
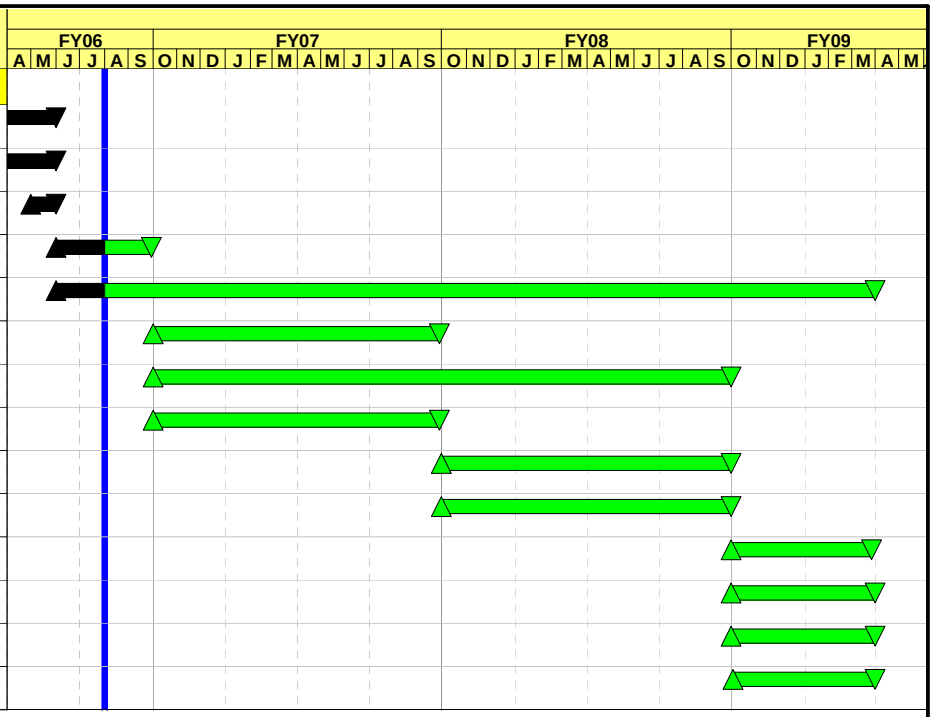
Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2.01.03.03 Project Mgmnt, Planning and Admn - M&S (OPC)				
PM210_0450	Physics Progammatic Travel	845	10/03/05A	05/31/06A
PM210_0470	SAC/FAC Travel	845	10/03/05A	05/31/06A
PM210_0990	M&S Supplies	107	05/01/06A	05/31/06A
PM400_0042	Education/Outreach M&S - FY06 Remainder	85*	06/01/06A	09/29/06
PM210_0451	Physics Progammatic Travel Rem	688*	06/01/06A	03/30/09
PM213_0114	SLAC Project Office Consumables- FY07	242	10/02/06	09/28/07
PM400_0043	Education/Outreach M&S - FY07-08	485	10/02/06	09/30/08
PM210_0480	Pre-ops Electrical Power Usage- 2007	241	10/03/06*	09/28/07
PM210_0490	Pre-ops Electrical Power Usage - 2008	242	10/01/07	09/29/08
PM213_0116	SLAC Project Office Consumables- FY08	243	10/01/07	09/30/08
PM210_0495	Pre-ops Electrical Power Usage - 2009	118	09/30/08	03/27/09
PM213_0117	SLAC Project Office Consumables- FY09	118	10/01/08	03/30/09
PM400_0044	Education/Outreach M&S - FY09	118	10/01/08	03/30/09
PM210_0497	Additional Startup Costs-FY09	117	10/02/08*	03/30/09
